



JOB No.: TCS01062/19

**EPD CONTRACT NO. EP/SP/86/15
ORGANIC WASTE TREATMENT FACILITIES PHASE 2**

**QUARTERLY ENVIRONMENTAL MONITORING AND
AUDIT (EM&A) SUMMARY REPORT
(SEPTEMBER TO NOVEMBER 2023)**

**PREPARED FOR
AJA JOINT VENTURE**

Date	Reference No.	Prepared By	Certified By
13 December 2023	TCS01062/19/600/R0351v1	 Martin Li (Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	13 December 2023	First Submission

Your ref TCS1062/19/300/L0352
Our ref 271491/02-09/RC/VH/NL-5570
File ref 02-09

ARUP

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong
Kowloon
Hong Kong

t +852 2528 3031

d +852 2268 3437

f +852 2268 3380

ricky-kh.chui@arup.com

www.arup.com

BY EMAIL (samuel.wu01@cohl.com)

AJA Joint Venture
5/F, Tower A, Manulife Financial Centre
223-231 Wai Yip Street
Kwun Tong, Kowloon
Hong Kong

Attn: Mr. Samuel Wu

19 December 2023

Dear Sir

Contract No. EP/SP/86/15
Organic Waste Treatment Facilities Phase 2
Quarterly Environmental Monitoring & Audit Report (September to November 2023)

Referring to your report referenced above dated 18 December 2023, we hereby verify that the captioned report ref. no. TCS01062/19/600/R0351v1 complied in general with the requirements as set out in the EM&A Manual.

Should you have any queries, please contact the undersigned at 2268 3437.

Yours faithfully



Ricky Chui
Independent Environmental Checker

cc EPD – Ms. Winnie Chu, Mr. Sunny Chiu, Mr. Jason Tsang, Mr. Julian Lam
Mr. W.W. Lau, Mr. Peter Wong, Mr. Gilbert Wong, Mr. David Ng
AECOM – Mr. Desmond Ng, Mr. Ben Tsang, Mr. Philip Cheung
Mr. K. C. Chu, Mr. Ivan Yung, Mr. YW Mok, Ms. Karie Ng
Mr. W.W. Tong, Ms. Rachel Zu
AJA JV – Ms. Tso So Fong, Mr. Tse Man Kit, Mr. Salinda Palipana
Ms. Beth Biddle, Mr. Gabriel Wong
AUES – Mr. T.W. Tam, Mr. Martin Li

EXECUTIVE SUMMARY

ES01 This is the 16th Quarterly Environmental Monitoring and Audit (EM&A) Summary Report for the Service Contract to summarized environmental monitoring results and inspection findings during the period from **1 September to 30 November 2023** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES02 Environmental monitoring activities under the EM&A program in this Reporting Period are summarized in the following table.

Table ES-1 Summary of Environmental Monitoring Activities Undertaken in the Reporting Period

Issues	Environmental Monitoring Parameters / Inspection	Sessions
Construction Noise	Leq (30min) Daytime	48
Construction Noise during Restricted Hours	Leq (5min) during restricted hours 19:00-07:00 including public holidays and Sundays	104
Inspection / Audit	ET Regular Environmental Site Inspection	13

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES03 No construction noise monitoring exceedance was recorded in this Reporting Period. The statistics of environmental exceedance and investigation of exceedance are summarized in the following table.

Table ES-2 Summary of Environmental Monitoring Parameter Exceedance in the Reporting Period

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action	
				Investigation Results	Corrective Actions
Construction Noise	Leq _{30min} Daytime	0	0	NA	NA
	Leq _{5min} Restricted hour	0	0	NA	NA

SITE INSPECTION

ES04 During the Reporting Period, weekly joint site inspections were undertaken to evaluate the site environmental performance. No non-compliances were observed during the weekly site inspection and environmental audit of the Reporting Period. Minor deficiencies found in the weekly site inspection were in general rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.

ENVIRONMENTAL COMPLAINT

ES05 No environmental complaint was recorded in this Reporting Period for the Project. The statistics of environmental complaint are summarized in the following table.

Table ES-3 Summary of Environmental Complaint Records in the Reporting Period

Reporting Period	Environmental Complaint Statistics			Related with the Works Contract
	Frequency	Cumulative	Complaint Nature	
1 – 30 September 2023	0	7	NA	NA
1 – 31 October 2023	0	7	NA	NA
1 – 30 November 2023	0	7	NA	NA

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES06 No environmental summons or prosecutions was received in this Reporting Period for the Project. The statistics of environmental summons or prosecutions are summarized in the following tables.

Table ES-4 Summary of Environmental Summons Records in the Reporting Period

Reporting Period	Environmental Summons Statistics			Related with the Works Contract
	Frequency	Cumulative	Complaint Nature	
1 – 30 September 2023	0	0	NA	NA
1 – 31 October 2023	0	0	NA	NA
1 – 30 November 2023	0	0	NA	NA

Table ES-5 Summary of Environmental Prosecutions Records in the Reporting Period

Reporting Period	Environmental Prosecution Statistics			Related with the Works Contract
	Frequency	Cumulative	Complaint Nature	
1 – 30 September 2023	0	0	NA	NA
1 – 31 October 2023	0	0	NA	NA
1 – 30 November 2023	0	0	NA	NA

REPORTING CHANGE

ES07 No reporting change was made in this Reporting Period.

FUTURE KEY ISSUES

ES08 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants should be implemented in accordance with the EM&A requirement.

ES09 In addition, all effluent discharge from the construction site shall fulfill the discharge licence stipulation.

Table of Contents

1. INTRODUCTION	1
1.1 PROJECT BACKGROUND	1
1.2 REPORT STRUCTURE	1
2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.1 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.2 CONSTRUCTION PROGRESS	2
2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS	2
3. SUMMARY OF IMPACT MONITORING REQUIREMENTS	4
3.1 GENERAL	4
3.2 MONITORING PARAMETERS	4
3.3 MONITORING LOCATIONS	4
3.4 MONITORING FREQUENCY AND PERIOD	4
3.5 MONITORING EQUIPMENT	4
3.6 ACTION/LIMIT (A/L) LEVELS	5
4. CONSTRUCTION NOISE MONITORING	6
4.1 GENERAL	6
4.2 RESULTS OF NOISE MONITORING	6
5. WASTE MANAGEMENT	7
5.1 GENERAL WASTE MANAGEMENT	7
5.2 RECORDS OF WASTE QUANTITIES	7
6. SITE INSPECTION	8
6.1 REQUIREMENTS	8
6.2 FINDINGS / DEFICIENCIES DURING THE REPORTING PERIOD	8
7. ENVIRONMENTAL COMPLAINT, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS	9
7.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	9
ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE	10
7.2 GENERAL REQUIREMENTS	10
8. CONCLUSIONS AND RECOMMENDATIONS	11
8.1 CONCLUSIONS	11
8.2 RECOMMENDATIONS	11

LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE PROJECT
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	IMPACT MONITORING STATIONS - CONSTRUCTION NOISE
TABLE 3-3	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 4-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 4-2	SUMMARY OF ADDITIONAL NOISE MONITORING RESULTS DURING RESTRICTED HOURS
TABLE 4-3	SUMMARIES OF CONSTRUCTION NOISE ACTION/LIMIT LEVEL EXCEEDANCE
TABLE 5-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 5-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 6-1	SITE OBSERVATIONS DURING THE WEEKLY INSPECTION
TABLE 7-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 7-2	STATISTICAL SUMMARY OF NOTIFICATION OF SUMMONS
TABLE 7-3	STATISTICAL SUMMARY OF SUCCESSFUL PROSECUTION
TABLE 8-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION CHART
APPENDIX C	MONITORING LOCATIONS FOR IMPACT MONITORING
APPENDIX D	3-MONTH ROLLING CONSTRUCTION PROGRAMME
APPENDIX E	GRAPHICAL PLOTS OF MONITORING RESULTS
APPENDIX F	METEOROLOGICAL INFORMATION
APPENDIX G	WASTE FLOW TABLE
APPENDIX H	ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

1. INTRODUCTION

1.1 PROJECT BACKGROUND

1.1.1 Environmental Protection Department (hereinafter referred as “EPD”) is the Project Proponent for the Project “*Organic Waste Treatment Facilities Phase 2*” (hereinafter referred as “the Project”). The Project is a Designated Project to be implemented under Environmental Permit No. EP-460/2013 (hereinafter referred as “the EP”). The major construction work of the Project included:

- (i) Demolition and removal of the existing above ground structures of the Sha Ling Livestock Waste Composting Plant (SLCP);
- (ii) Construction of superstructure for an administration building and enclosed waste reception area;
- (iii) Installation of treatment facilities including waste pre-treatment equipment, digesters, biogas holding tanks, composting, wastewater treatment, air treatment systems; and
- (iv) Facilities for biogas processing, utilization and transmission;

1.1.2 AJA Joint Venture (hereinafter referred as “AJAJV”) has been awarded the *EPD Contract No. EP/SP/86/15 “Organic Waste Treatment Facilities Phase 2”*. In accordance with the Works Contract requirements, AJAJV shall take over the responsibility of the EP. Based on the requirement, Further Environmental Permit application was submitted by AJAJV to EPD on 10 September 2019 and granted on 2 October 2019. A variation of Further Environmental Permit was submitted on 21 August 2020 and granted on 14 September 2020. The Further Environmental Permit is named as FEP-01/460/2013/A.

1.1.3 According to the approved Environmental Monitoring and Audit Manual (hereinafter referred as “the EM&A Manual”), AJAJV employed Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) as Environmental Team (hereinafter referred as “ET”) to implement monitoring programme and as well as the associated duties.

1.1.4 According to the EM&A Manual, construction noise was identified as the only key environmental issue during the construction phase of the Project and it is required to carry out construction noise monitoring throughout the construction phase. Furthermore, baseline noise monitoring as part of the EM&A programmes shall be conducted prior to the commencement of the construction works under the Project. Thus, baseline noise monitoring was conducted by ET from **25 September 2019** to **8 October 2019**. The baseline monitoring report compiled by the ET was verified by Independent Environmental Checker (hereinafter the “IEC”) and was submitted to EPD on 19th November 2019 for endorsement.

1.1.5 This is the **16th** Quarterly EM&A Summary Report for the Service Contract to summarized monitoring results and inspection findings during the period from **1 September to 30 November 2023** (hereinafter ‘the Reporting Period’).

1.2 REPORT STRUCTURE

1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

Section 1	<i>Introduction</i>
Section 2	<i>Project Organization and Construction Progress</i>
Section 3	<i>Summary of Impact Monitoring Requirements</i>
Section 4	<i>Construction Noise Monitoring</i>
Section 5	<i>Waste Management</i>
Section 6	<i>Site Inspections</i>
Section 7	<i>Environmental Complaints and Non-Compliance</i>
Section 8	<i>Implementation Status of Mitigation Measures</i>
Section 9	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1.1 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#). Details of responsibilities of respective parties can be referred to EM&A Monthly Report.

2.2 CONSTRUCTION PROGRESS

2.2.1 3-month rolling construction program of the Project is enclosed in [Appendix D](#); and the major construction activities undertaken in the Reporting Period is presented as below:

September 2023

- Granulation Building
 - Internal ABWF works & E&M work
- Admin Building
 - External ABWF works & E&M work
- Reception Building
 - External/Internal ABWF works & E&M work
- AD Tanks
 - Watertightness testing for AD1, AD2, AD3 and AD4
- Footbridge – ABWF Works

October 2023

- Granulation Building
 - ABWF works
 - E&M work at Granulation Hall and underground water tanks
- Admin Building
 - ABWF works and E&M work
- Reception Building
 - ABWF works and E&M work
- AD Tanks
 - Watertightness testing for AD1, AD2, AD3 and AD4
 - Installation of steel link bridges between tanks
- Digestate Tank – Tank base screeding preparation
- Pump House – External ABWF Work

November 2023

- Granulation Building
 - ABWF works
 - E&M work at Granulation Hall and underground water tanks
- Admin Building
 - ABWF works and E&M work
- Reception Building
 - ABWF works and E&M work
- AD Tanks
 - Coating work for AD1, AD2 and AD4
 - Concrete screeding work for AD3
- Digestate Tank – Concrete screeding work
- Pump House – External ABWF Work

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project of contract 1 are presented in *Tables 2-1*.

Table 2-1 Status of Environmental Licenses and Permits of the Project

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Notification pursuant to Air pollution Control (Construction Dust) Regulation	Application No. 448863	9 Sep 2019	NA	Valid
2	Chemical Waste Producer Registration	Ref. No. 5211-641-A295 7-01	9 Oct 2019	NA	Valid
3	Water Pollution Control Ordinance - Discharge License	Application No. 448913	--	--	Application made on 10 Sep 2019
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account No. 7035307	2 Oct 2019	NA	Valid
5	Further Environmental Permit	FEP-01/460/201 3/A	14 Sep 2020	NA	Valid
6	Construction Noise Permit	GW-RN0721-23	6 Jul 2023	5 Oct 2023	Valid until 5 Oct 2023
		GW-RN1043-23	6 Oct 2023	5 Feb 2024	Valid
7	Waste Water Discharge License	WT00035196-2 019	20 Mar 2020	31 Mar 2025	Valid

3. SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 According to Environmental Monitoring and Audit requirements set out in the Approved EM&A manual, construction noise was identified as the only key environmental issues during the construction phase of the Project.

3.2 MONITORING PARAMETERS

3.2.1 The construction noise monitoring requirement stated in the approved EM&A Manual is summarized in *Table 3-1*.

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters
Noise	<ul style="list-style-type: none"> Leq(30min) in normal working days (Monday to Saturday) 07:00-19:00 except public holiday Supplementary information for data auditing, statistical results such as L₁₀ and L₉₀ shall also be obtained for reference Leq(5min) if construction works are extended to restricted hours 19:00-07:00 including public holidays and Sundays

3.3 MONITORING LOCATIONS

3.3.1 According to the EM&A Manual Section 4.2.3, four (4) designated noise sensitive receivers (NSR) were recommended as construction noise monitoring stations. Since two of the designated monitoring locations N2 and N3 were found not accessible, alternative monitoring locations N2a and N3a were therefore proposed for the noise monitoring and were approved by EPD on 1 June 2021. Details of the locations for construction noise monitoring in the Reporting Period is listed in *Table 3-2* and showed in *Appendix C*.

Table 3-2 Impact Monitoring Stations – Construction Noise

ID	Location
N1	Village House No. 308, Sha Ling
N2a	Village House No. 318, Sha Ling
N3a	Village House No. 261, Sha Ling
N4	Village House in Sha Ling

3.4 MONITORING FREQUENCY AND PERIOD

3.4.1 Noise monitoring shall be conducted at the all available designated monitoring stations or alternative locations. The monitoring frequency shall depend on scale of the construction activities. According to EM&A manual, regular noise monitoring should be carried out once a week when noise generating activities are underway and the monitoring requirement is presented below:

- one set of Leq_(30min) measurements between 07:00 and 19:00 hours on normal weekdays

3.4.2 If construction works are extended to restricted hours 19:00-07:00 in normal working days (Monday to Saturday), and 00:00-24:00 during public holidays including Sunday, additional weekly impact monitoring should be carried out during the respective restricted hour periods. Leq_(5min) measurements should be employed during the restricted hours.

3.5 MONITORING EQUIPMENT

3.5.1 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms⁻¹.

3.6 ACTION/LIMIT (A/L) LEVELS

3.6.1 Action and Limit levels for construction noise as stipulated in the approved Environmental Monitoring and Audit Manual are listed in *Tables 3-3*.

Table 3-3 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
Time Period:	0700-1900 hours on normal weekdays	
N1	When one or more documented complaints are received	75 dB(A)
N2a		
N3a		
N4		
Time Period:	19:00-07:00 in normal working days (Monday to Saturday), and 00:00-24:00 during public holidays including Sunday	
N1	When one or more documented complaints are received	60 dB(A)
N2a		
N3a		
N4		

Note: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority should be followed.

4. CONSTRUCTION NOISE MONITORING

4.1 GENERAL

4.1.1 In the Reporting Period, construction noise monitoring was performed at monitoring location N1, N2a, N3a and N4.

4.2 RESULTS OF NOISE MONITORING

4.2.1 In the Reporting Period, a total of **48** sessions of daytime construction noise monitoring and **104** sessions of additional weekly noise monitoring during restricted hours were performed at the agreed monitoring locations in the reporting period. The daytime noise monitoring results and additional weekly noise monitoring results during restricted hours are summarized in **Table 4-1** and **Table 4-2**, respectively. The graphical plots of construction noise monitoring result are shown in **Appendix E**.

Table 4-1 Summary of Construction Noise Monitoring Results

Monitoring Location	Leq, 30min (dB(A))	
	Min	Max
N1	52.5	66.4
Record Date	27-Oct-23	20-Nov-23
N2a	49.7	59.8
Record Date	20-Sep-23	9-Sep-23
N3a	59.1	71.5
Record Date	27-Oct-23, 8-Nov-23	9-Sep-23
N4	49.5	68.6
Record Date	8-Nov-23	20-Nov-23

Table 4-2 Summary of Additional Noise Monitoring Results during Restricted Hours

Monitoring Location	Leq, 5min (dB(A))	
	Min	Max
N1	47.1	59.3
Record Date	19-Sep-23, 11-Oct-23	13-Nov-23
N2a	43.8	56.3
Record Date	3-Oct-23	19-Sep-23
N3a	49.5	59.2
Record Date	11-Oct-23	1-Oct-23
N4	43.1	56.3
Record Date	3-Oct-23	20-Nov-23

4.2.2 As shown in **Table 4-1**, all the measured results during normal daytime were below 75 dB(A) of the acceptance criteria. In addition, all the measured results during restricted hours shown in **Table 4-2** were below 60 dB(A) of the acceptance criteria as set out in Technical Memorandum on Noise from Construction Work other than Percussive Piling. No adverse weather condition which may affect the monitoring result was encountered during the course of noise monitoring in the reporting period.

4.2.3 No documented noise complaint is received in the reporting period. Hence no construction noise monitoring action level exceedance was recorded.

4.2.4 Summary of A/L Level exceedance of construction noise and statistical analysis of compliance for construction noise monitoring results are summarized in **Table 4-3**.

Table 4-3 Summaries of Construction Noise Action/Limit Level Exceedance

Station	Limit Level	Action Level	Received Date
N1	0	0	NA
N2a	0		
N3a	0		
N4	0		

5. WASTE MANAGEMENT

5.1 GENERAL WASTE MANAGEMENT

5.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

5.2 RECORDS OF WASTE QUANTITIES

5.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

5.2.2 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 5-1* and *5-2*.

Table 5-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity			Disposal Location
	Sep 2023	Oct 2023	Nov 2023	
Total C&D Materials (Inert) ('000m ³)	0	0	0.052	-
Reused in this Contract (Inert) ('000m ³)	0	0	0	-
Reused in other Projects (Inert) ('000m ³)	0	0	0	-
Disposal as Public Fill (Inert) ('000m ³)	0	0	0.052	TM38

Table 5-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity			Disposal Location
	Sep 2023	Oct 2023	Nov 2023	
Recycled Metal ('000kg)	0	0	0	-
Recycled Paper / Cardboard Packing ('000kg)	0	0	0	-
Recycled Plastic ('000kg)	0	0	0	-
Chemical Wastes ('000kg)	0	0	0	-
General Refuses ('000m ³)	0.052	0.057	0.075	NENT

6. SITE INSPECTION

6.1 REQUIREMENTS

6.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulated by ET Leader. Weekly environmental site inspections should be carried out to confirm the environmental performance.

6.2 FINDINGS / DEFICIENCIES DURING THE REPORTING PERIOD

6.2.1 In the Reporting Period, **13** events of joint site inspection by the Employer’s Representative (ER), ET, IEC and the Contractor were undertaken for the Contract to evaluate the site environmental performance. No non-compliance was identified during the site inspection. The summaries of findings / deficiencies recorded in the site inspection during the Reporting Period are presented in **Table 6-1**.

6.2.2 The findings / deficiencies of the Project observed during the weekly site inspection are listed in **Table 6-1**.

Table 6-1 Summary of Reminders/Observations of Site Inspection in Reporting Period

Reporting Period	Date of site inspection	Nos. of findings / reminders	Follow-Up Status
September 2023	6, 13, 20 and 27 September 2023	3	Completed
October 2023	4, 11, 18 and 25 October 2023	5	Completed
November 2023	1, 8, 15, 22 and 29 November 2023	7	Completed

7. ENVIRONMENTAL COMPLAINT, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

7.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

7.1.1 In the Reporting Period, no environmental complaint, summons and prosecution under the EM&A Programme was lodged for the project. The statistical summary table of environmental complaint is presented in Tables 7-1, 7-2 and 7-3.

Table 7-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
September 2023	0	7	NA
October 2023	0	7	NA
November 2023	0	7	NA

Table 7-2 Statistical Summary of Notification of Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Summons Nature
September 2023	0	0	NA
October 2023	0	0	NA
November 2023	0	0	NA

Table 7-3 Statistical Summary of Successful Prosecutions

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Prosecution Nature
September 2023	0	0	NA
October 2023	0	0	NA
November 2023	0	0	NA

ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

7.2 GENERAL REQUIREMENTS

- 7.2.1 The environmental mitigation measures that recommended in the Environmental Mitigation Implementation Schedule (EMIS) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in *Appendix H*.
- 7.2.2 AJAJV had been implementing the required environmental mitigation measures according to the Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by AJAJV in this Reporting Period are summarized in *Table 8-1*.

Table 8-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> • Any wastewater generated should be appropriately treated by treatment facilities; • Drainage channels were provided to convey run-off into the treatment facilities; and • Drainage systems were regularly and adequately maintained.
Air Quality	<ul style="list-style-type: none"> • Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; • Frequent watering for particularly dusty construction areas and areas close to air sensitive receivers; • Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet; • Public roads around the site entrance/exit had been kept clean and free from dust; and • Tarpaulin covering of any dusty materials on a vehicle leaving the site.
Noise	<ul style="list-style-type: none"> • Good site practices to limit noise emissions at the sources; • Use of quiet plant and working methods; • Use of site hoarding or other mass materials as noise barrier to screen noise at ground level of NSRs; • Use of shrouds/temporary noise barriers to screen noise from relatively static PMEs; • Alternative use of plant items within one worksite, where practicable.
Waste Management	<ul style="list-style-type: none"> • Any excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; • Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; • Trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill was implemented; and • Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
General	<ul style="list-style-type: none"> • The site was generally kept tidy and clean.

8. CONCLUSIONS AND RECOMMENDATIONS

8.1 CONCLUSIONS


- 8.1.1 This is the **16th** Quarterly Environmental Monitoring and Audit (EM&A) Summary Report for the Service Contract to summarized monitoring results and inspection findings during the period from **1 September to 30 November 2023** (the Reporting Period).
- 8.1.2 In the Reporting Period, no construction noise limit level exceedance during daytime and restricted hours was recorded and no noise complaint (which is an Action Level exceedance) was received by the ER, EPD and the Contractors.
- 8.1.3 During the Reporting Period, weekly joint site inspections were undertaken to evaluate the site environmental performance. No non-compliances were observed during the weekly site inspection and environmental audit of the Reporting Period. Minor deficiencies found in the weekly site inspection were in general rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.
- 8.1.4 No documented complaint, notification of summons or successful prosecution was received under the Project.

8.2 RECOMMENDATIONS

- 1.2.1 Construction noise should be a key environmental impact during the works. The noise mitigation measures such as use of quiet plants or temporary noise barrier installation at the construction noise predominated area should be implemented in accordance with the EM&A requirement and the latest CNP.
- 8.2.1 In addition, all effluent discharge shall be ensured to fulfill the discharge license stipulation.
- 8.2.2 All the trees proposed to be retained in-situ should be properly preserved and protected during the construction works. Tree Preservation and Protection Works for these retained trees shall follow Section 3 and 26 of CEDD's General Specification for Engineering Works and Section 26 of Contract Specification Part B.
- 8.2.3 Trees to be felled shall be in accordance with the Tree Preservation and Removal Proposal (TPRP) to be approved by relevant approval authority. The tree removal work shall only commence after such approval has been granted.
- 8.2.4 Contract Specification Part B Section 1.78 "Waste Management" and DEVB's "Guidelines on Yard Waste Reduction and Treatment" should be referred before tree removal and plan the necessary arrangement.


Appendix A

Layout plan of the Project

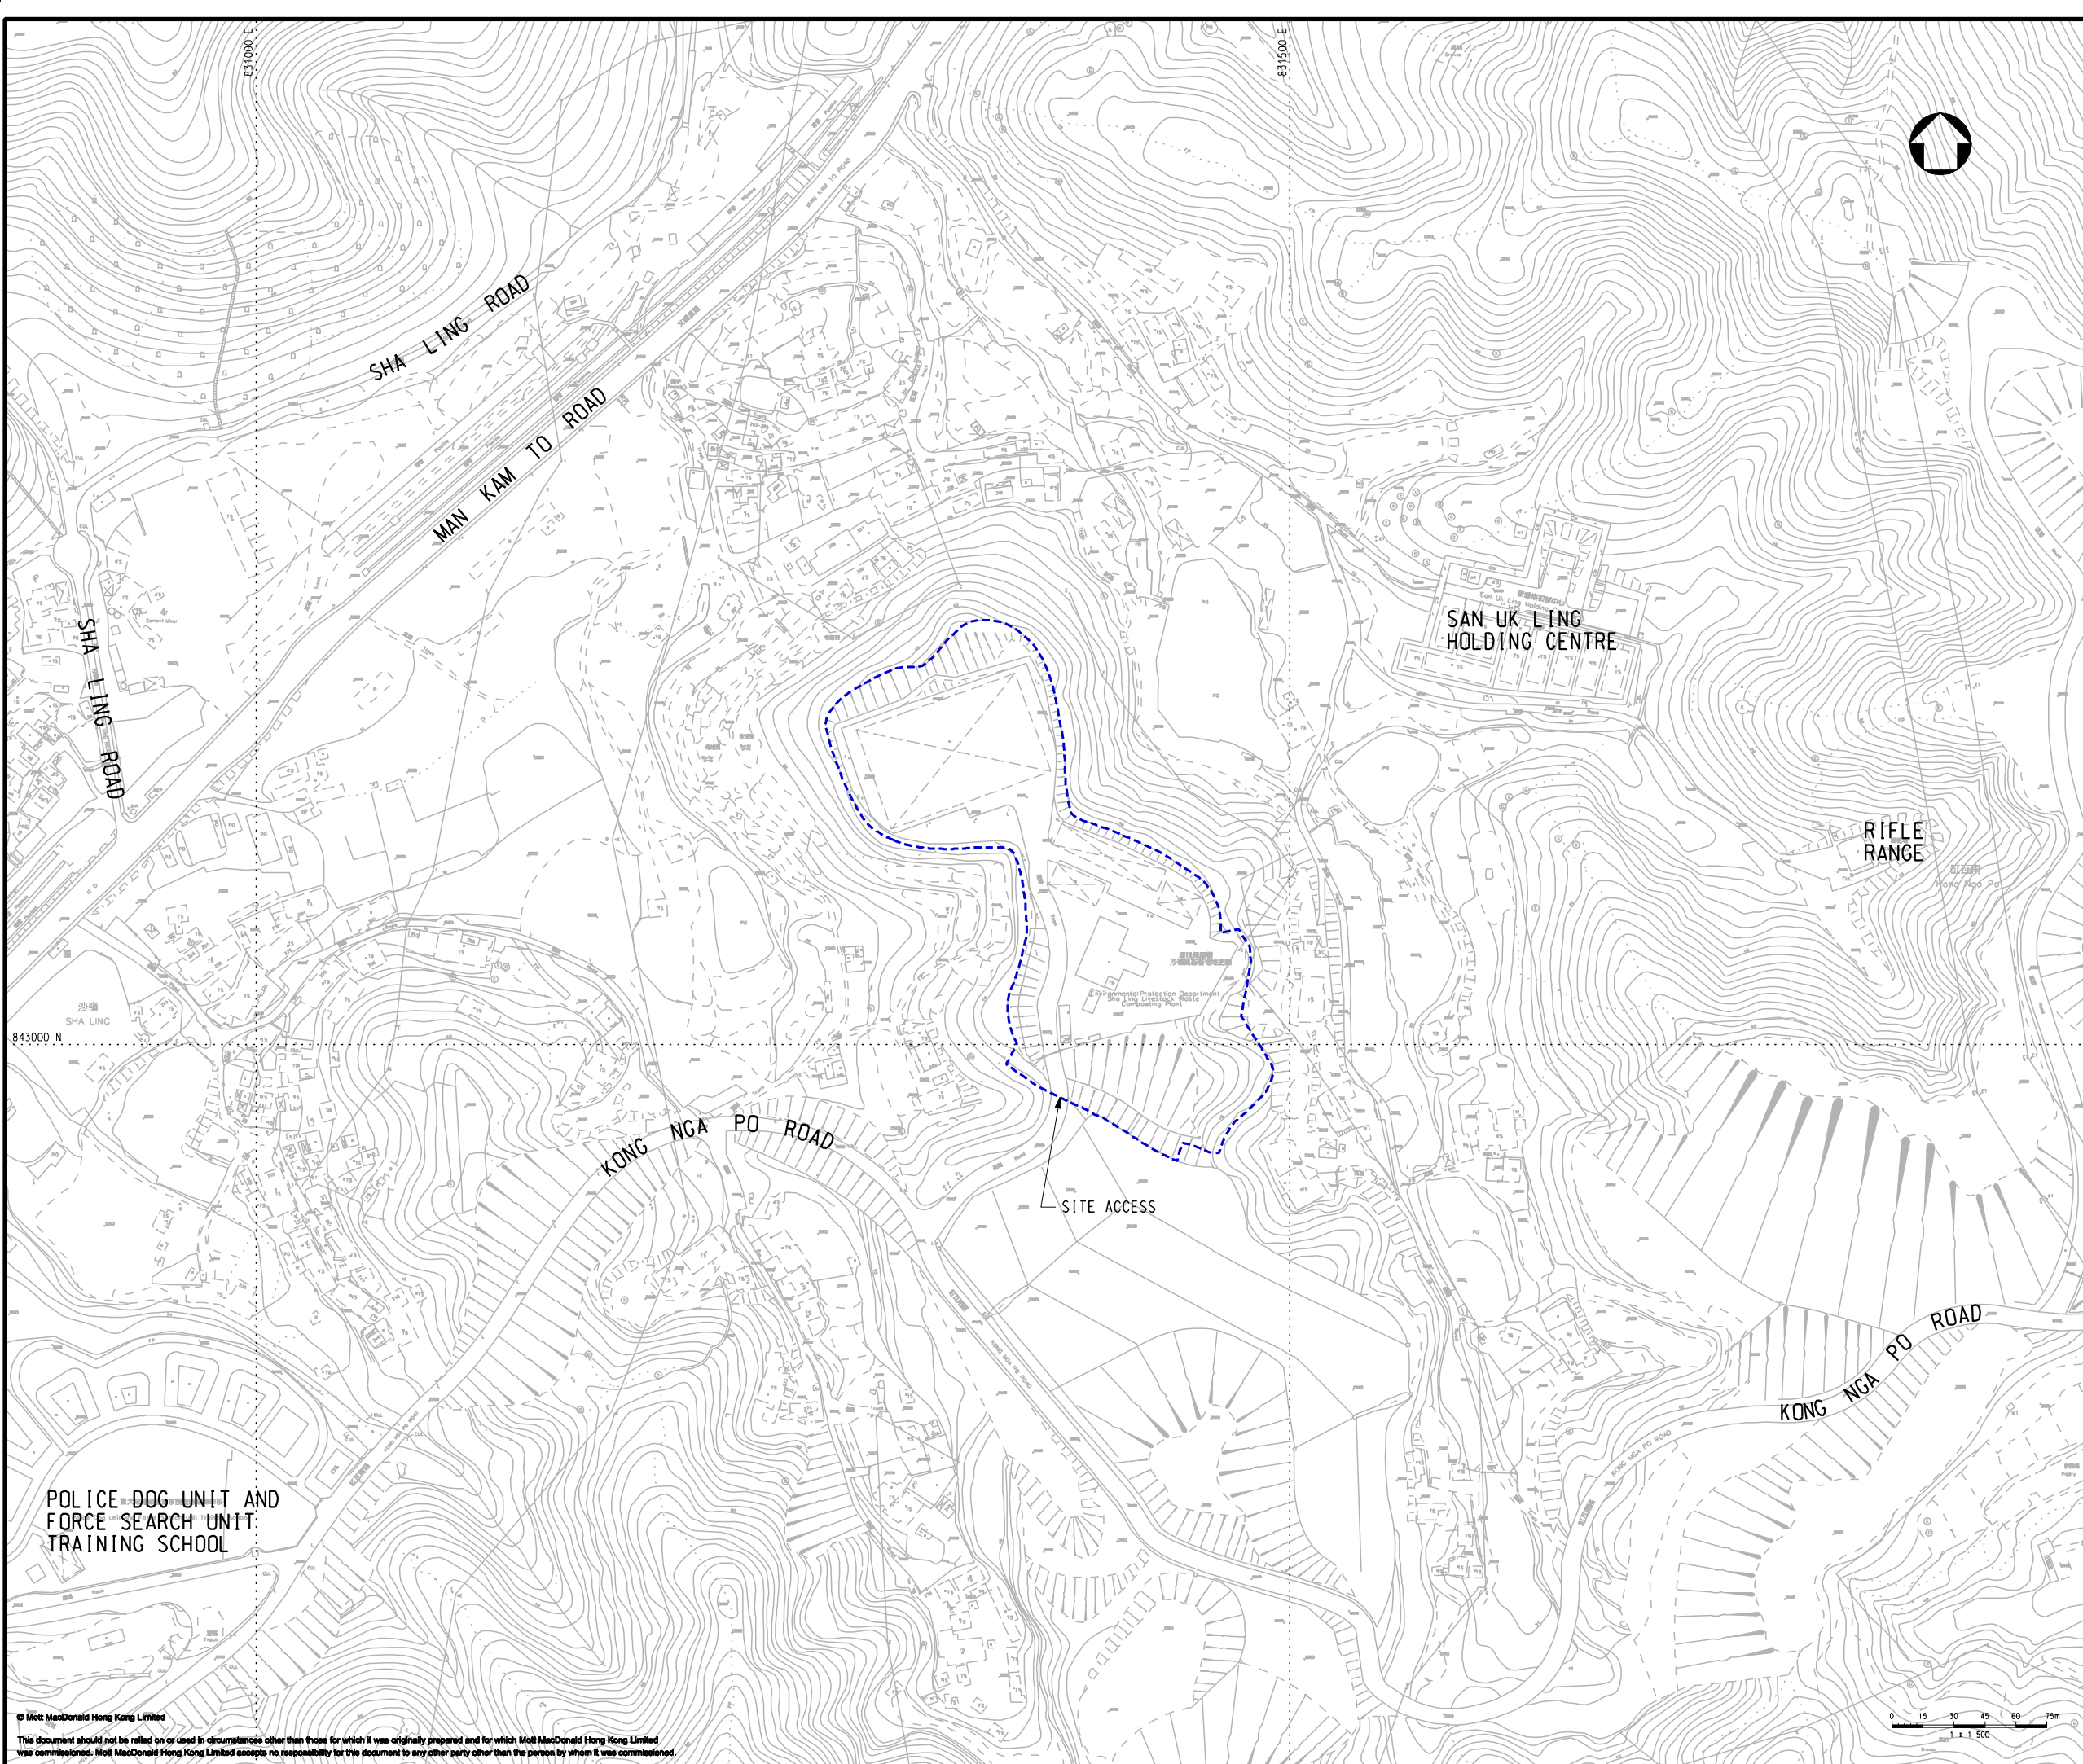


Notes

Key to symbols

 PROPOSED SITE AREA

Reference drawings

Rev	Date	Drawn	Description	Ch'k'd	App'd
P2	JUN 13	MING	GENERAL REVISION	MR	AFK
P1	DEC 12	MING	FIRST ISSUE	MR	AFK



20/F Two Landmark East
100 How Ming Street
Kowloon
Hong Kong
T +852 2828 8757
F +852 2827 1823
www.mottmac.com.hk

Client



Environmental Protection Department
The Government of the Hong Kong
Special Administrative Region

Project

**AGREEMENT NO. CE34/2011(EP)
DEVELOPMENT OF ORGANIC WASTE
TREATMENT FACILITIES PHASE 2 -
FEASIBILITY STUDY**

Title


LOCATION OF THE PROJECT

Designed	HY	Eng check	AT
Drawn	MING	Coordination	AT
Dwg check	HY	Approved	AFK
Scale at A1	1:1500	Status	PRE
Drawing Number		Rev	P2

FIGURE 1.1

Appendix B
Organization Chart

Project Organization Chart

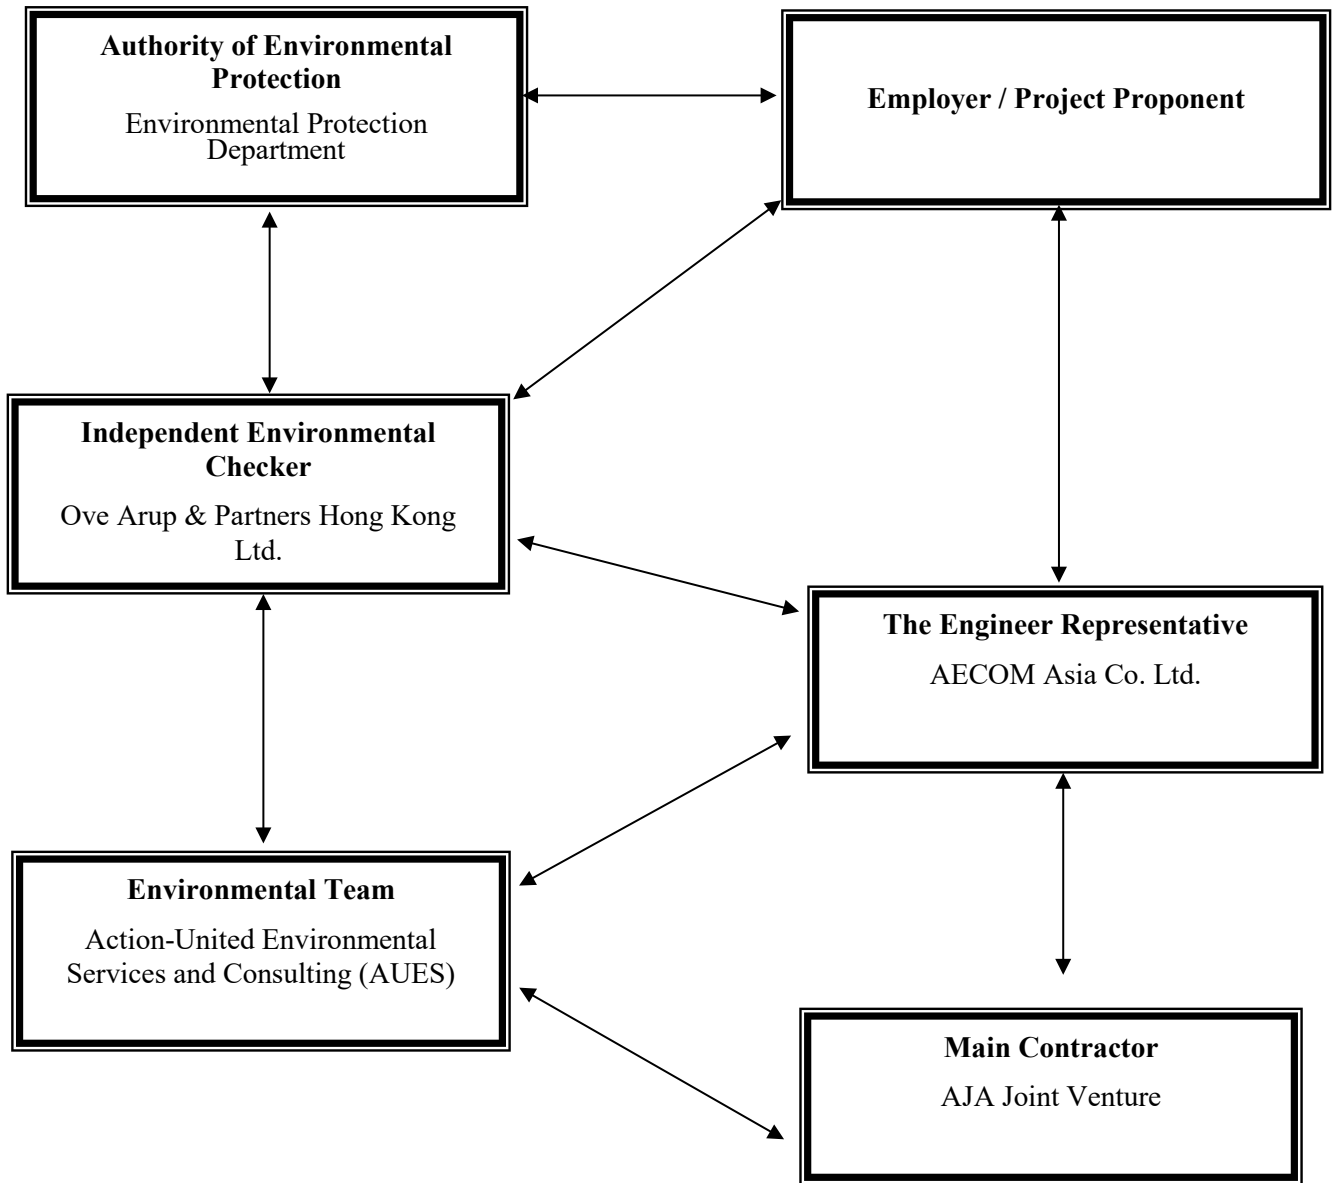

Contact Details of Key Personnel for the Project

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
EPD	Project Proponent	Sunny Chiu	3151 7209	3528 0492
AECOM	Resident Engineer	Terrence Lam	5579 5239	3010 8507
AECOM	Resident Engineer	Ivan Yung	5723 7750	3010 8507
ARUP	Independent Environmental Checker	Ricky Chui	2268 3437	2268 3380
ARUP	Engineer (Safety, Environment and Planning)	Roy Ng	2268 3588	2268 3588
AJAJV	Project Manager	Victor Wu	2862 5013	2862 5013
AJAJV	Construction Manager	Ethan Wong	9805 7325	9805 7325
AJAJV	Project Environmental Manager	Samuel Tsui	9455 5865	9455 5865
AJAJV	Environmental Officer	Harry Lam	9353 6141	9353 6141
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Martin Li	2959 6059	2959 6079

Legend:

EPD (Employer) – Environmental Protection Department

AECOM (Project Consultant) – AECOM Asia Co. Ltd.


AJAJV (Main Contractor) – AJA Joint Venture

ARUP (IEC) – Ove Arup & Partners Hong Kong Ltd.

AUES (ET) – Action-United Environmental Services & Consulting

Appendix C

Monitoring Locations for Impact Monitoring

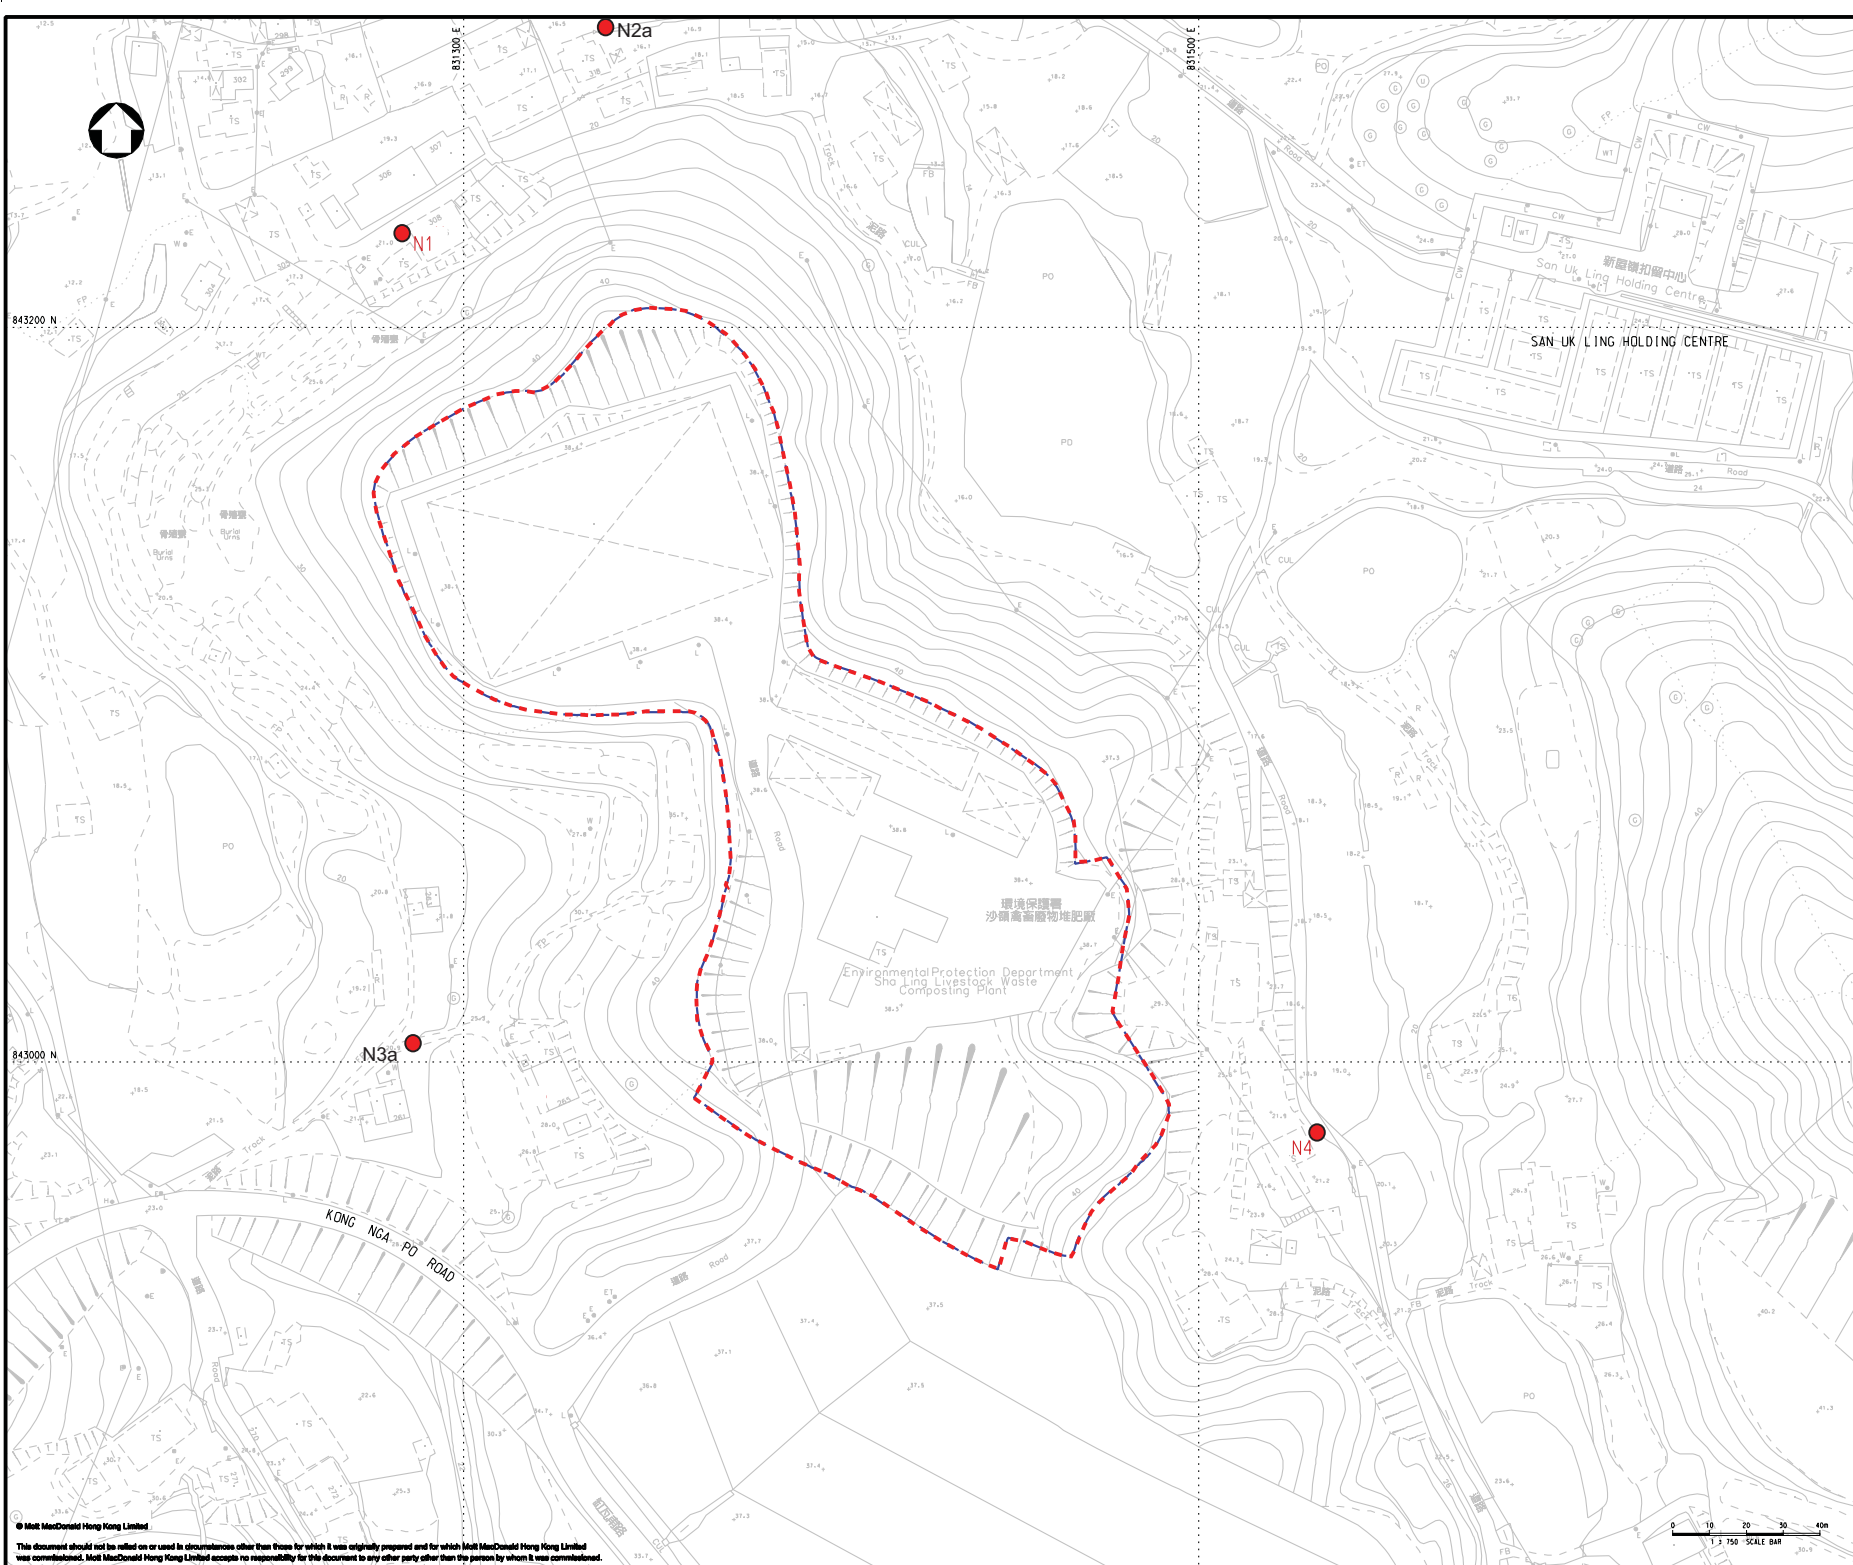

Notes

Key to symbols

- - - - - Construction Site Boundary
- Noise Monitoring Station

Reference drawings

P2	JUL 13	MING	GENERAL REVISION	AM	AFK
P1	DEC 12	MING	FIRST ISSUE	SC	AFK
Rev	Date	Drawn	Description	Chk'd	App'd

--	--	--	--	--	--



20F Two Landmark East
100 How Ming Street
Kowloon, Hong Kong
T +852 2828 8787
F +852 2827 1823
www.mottmac.com.hk

Client



Environmental Protection Department
The Government of the Hong Kong
Special Administrative Region

Project
AGREEMENT NO. CE34/2011(EP)
DEVELOPMENT OF ORGANIC WASTE
TREATMENT FACILITIES PHASE 2 -
FEASIBILITY STUDY

Title
PROPOSED LOCATIONS OF
CONSTRUCTION NOISE
MONITORING STATIONS

Designed	SC	Eng check	AT
Drawn	MING	Coordination	AT
Dwg check	EY	Approved	AFK
Scale at A1	1:750	Status	PRE
Drawing Number		Rev	P2

FIGURE 4.1

Appendix D

3-Month Rolling Construction Programme

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023			
						Sep	Oct	Nov	Dec
Contract No. EP/SP/86/15 - ORGANIC RESOURCE RECOVERY CENTRE, PHASE 2 (JULY 2022)						50	51	52	53
CIVIL, STRUCTURAL AND BUILDING WORKS									
RECEPTION BUILDING (INCLUDING ADMINISTRATION BUILDING)									
ABWF WORKS									
Lower Ground Floor									
O2_CS_RB0010	Conveyor Pit - Surface channel + Sump pit	9	16-Oct-23*	24-Oct-23	124		24-Oct-23		
O2_CS_RB0020	Conveyor Pit - Floor paint	3	25-Oct-23*	27-Oct-23	121		27-Oct-23		
Ground Floor									
O2_CS_RB0030	Display Area (R-G01) - Floor finish (Tiling Works)	8	12-Oct-23*	19-Oct-23	129	19-Oct-23			
O2_CS_RB0040	Display Area (R-G01) - FRR ceiling (replace damaged board)	8	01-Nov-23*	08-Nov-23	109		08-Nov-23		
O2_CS_RB0050	Display Area (R-G01) - Entrance glass door/glass panel	8	09-Nov-23*	16-Nov-23	101			16-Nov-23	
O2_CS_RB0060	Fireman's Lift Lobby 2 (R-G02) - Floor finish (Tiling Works)	8	12-Oct-23*	19-Oct-23	129	19-Oct-23			
O2_CS_RB0080	Lavatories (R-G09, G11, G12) - Wall (Furring + Tiling Works)	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0100	EL Room (R-G06) - Floor paint	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0110	ELV Room (R-G07) - Floor paint	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0120	Laboratory (R-G03) - floor finish	9	16-Oct-23*	24-Oct-23	124	24-Oct-23			
O2_CS_RB0130	Laboratory (R-G03) - Remaining wall	4	01-Nov-23*	04-Nov-23	113		04-Nov-23		
O2_CS_RB0140	Fire Control Centre (R-G05) - Floor paint	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0150	Contaminants Bays (R-G20) - Surface channel	8	12-Oct-23*	19-Oct-23	129	19-Oct-23			
O2_CS_RB0160	Contaminants Bays (R-G20) - Floor paint	4	01-Nov-23*	04-Nov-23	113		04-Nov-23		
O2_CS_RB0170	Contaminants Bunker (R-G21 G22) - Ucrete floor finish with dish channel	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0180	Air Compressor Room (R-G30) - Finish to retrofitted wall	8	23-Oct-23*	30-Oct-23	118		30-Oct-23		
O2_CS_RB0190	Air Compressor Room (R-G30) - Floor paint	4	31-Oct-23*	03-Nov-23	114		03-Nov-23		
O2_CS_RB0200	Process Water Pump Room (R-G28) - Finish to retrofitted wall	8	23-Oct-23*	30-Oct-23	118		30-Oct-23		
O2_CS_RB0210	Process Water Pump Room (R-G28) - Floor paint	4	31-Oct-23*	03-Nov-23	114		03-Nov-23		
O2_CS_RB0220	Grey Water Pump Room (R-G29) - Finish to retrofitted wall	8	23-Oct-23*	30-Oct-23	118		30-Oct-23		
O2_CS_RB0230	Grey Water Pump Room (R-G29) - Floor paint	4	31-Oct-23*	03-Nov-23	114		03-Nov-23		
O2_CS_RB0240	Unloading Bays (R-G24, G25, G26, G27) - Surface Channel	8	19-Oct-23*	26-Oct-23	122	26-Oct-23			
O2_CS_RB0250	Bin Unloading Bay 5/ Refuse Chamber (R-G32) - Surface Channel	8	01-Nov-23*	08-Nov-23	109		08-Nov-23		
O2_CS_RB0260	Bin Unloading Bay 5/ Refuse Chamber (R-G32) - Floor finish + floor paint	8	09-Nov-23*	16-Nov-23	101			16-Nov-23	
O2_CS_RB0270	Tanker Bay (R-G31) - Surface Channel	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0280	Tanker Bay (R-G31) - Ucrete floor finish	8	08-Nov-23*	15-Nov-23	102			15-Nov-23	
O2_CS_RB0290	Fireman's Lift Lobby 1 (R-G34) - Floor finish (Tiling Works)	8	20-Oct-23*	27-Oct-23	121		27-Oct-23		
O2_CS_RB0300	Store (R-G33) - Wall/ Ceiling finish	8	09-Oct-23*	16-Oct-23	132	16-Oct-23			
O2_CS_RB0310	Store (R-G33) - Floor Painting	4	17-Oct-23*	20-Oct-23	128	20-Oct-23			
O2_CS_RB0320	Lavatory (R-G35, G36) - Floor finish (Tiling Works)	5	24-Oct-23*	28-Oct-23	120		28-Oct-23		
O2_CS_RB0330	Lavatory (R-G35, G36) - Wall (Furring + Tiling Works)	10	29-Oct-23*	07-Nov-23	110		07-Nov-23		
O2_CS_RB0340	EVA passage - Baffle ceiling/ hanger wall	15	07-Nov-23*	21-Nov-23	96			21-Nov-23	
First Floor									
O2_CS_RB0350	Flat Roof (R-F12) - Waterproofing	4	01-Dec-23*	04-Dec-23	83				
O2_CS_RB0360	Flat Roof (R-F12) - Floor Screeding	4	05-Dec-23*	08-Dec-23	79				
O2_CS_RB0370	Flat Roof (R-F12) - Glass balustrade	7	09-Dec-23*	15-Dec-23	72				
O2_CS_RB0380	Manager Room (R-F02) - Glass panel	7	09-Dec-23*	15-Dec-23	72				
O2_CS_RB0410	Fireman's Lift Lobby 2 - Floor (Tiling Works)	12	28-Oct-23*	08-Nov-23	109		08-Nov-23		
O2_CS_RB0420	Fireman's Lift Lobby 2 - Wall Painting	4	09-Nov-23*	12-Nov-23	105			12-Nov-23	
O2_CS_RB0440	Canopy outside Operator Office - Waterproofing	3	14-Oct-23*	16-Oct-23	132	16-Oct-23			
O2_CS_RB0450	Canopy outside Operator Office - Floor Screeding	5	17-Oct-23*	21-Oct-23	127	21-Oct-23			
O2_CS_RB0460	Canopy outside Operator Office - Guard railing	8	22-Oct-23*	29-Oct-23	119	29-Oct-23			
O2_CS_RB0470	IT Room (R-F06) - Raised floor	13	28-Oct-23*	09-Nov-23	108		09-Nov-23		
O2_CS_RB0480	EL Room (R-F07) - Raised floor	13	28-Oct-23*	09-Nov-23	108		09-Nov-23		
O2_CS_RB0490	ELV Room (R-F08) - Raised floor	13	28-Oct-23*	09-Nov-23	108		09-Nov-23		
O2_CS_RB0510	Male Toilet (R-F09) - Wall (Furring + Tiling Works)	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0530	Male Toilet (R-F09) - Surface channel	8	31-Oct-23*	07-Nov-23	110		07-Nov-23		
O2_CS_RB0550	Female Toilet (R-F10) - Wall (Furring + Tiling Works)	8	24-Oct-23*	31-Oct-23	117		31-Oct-23		
O2_CS_RB0560	Female Toilet (R-F10) - Surface channel	8	31-Oct-23*	07-Nov-23	110		07-Nov-23		
O2_CS_RB0580	Corridor to R-ST3 (R-F14) - Floor finish (Grano)	8	07-Nov-23*	14-Nov-23	103			14-Nov-23	
O2_CS_RB0590	E/M Room (R-F20) - Floor finish	4	16-Oct-23*	19-Oct-23	129	19-Oct-23			
O2_CS_RB0610	Canopy along grille SJ - Waterproofing	4	01-Dec-23*	04-Dec-23	83				
O2_CS_RB0620	Canopy along grille SJ - Floor Screeding	4	05-Dec-23*	08-Dec-23	79				
Roof Floor									
O2_CS_RB0650	ELV Room (R-R12) - Raised floor	16	10-Nov-23*	25-Nov-23	92			25-Nov-23	
O2_CS_RB0660	LV Room (R-R13) - Raised floor	16	10-Nov-23*	25-Nov-23	92			25-Nov-23	
O2_CS_RB0670	Lactation Room 1 (R-R17A) - Raised floor	16	10-Nov-23*	25-Nov-23	92			25-Nov-23	
O2_CS_RB0680	Lactation Room 1 (R-R17B) - Raised floor	16	10-Nov-23*	25-Nov-23	92			25-Nov-23	
O2_CS_RB0690	Male Changing Room (R-R15) - Surface channel	8	27-Oct-23*	03-Nov-23	114		03-Nov-23		
O2_CS_RB0700	Male Changing Room (R-R15) - Remaining wall (Tiling Works)	8	01-Nov-23*	08-Nov-23	109		08-Nov-23		
O2_CS_RB0710	Male Changing Room (R-R15) - floor finish (Tiling Works)	8	01-Nov-23*	08-Nov-23	109		08-Nov-23		



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23
 Page 1 of 6

Legend:

- Remaining Work
- Remaining Work (Critical)
- Actual Work
- Level of Effort
- Baseline Milestone
- Start Milestone
- Finish Milestone

Contract No. EP/SP/86/15
Organic Waste Treatment Facilities, Phase 2
3 Months Rolling Programme

extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023					
						Sep	Oct	Nov	Dec		
O2_CS_RB0720	Female Changing Room (R-R16) - Surface channel	8	27-Oct-23*	03-Nov-23	114						
O2_CS_RB0730	Female Changing Room (R-R16) - Remaining wall	8	27-Oct-23*	03-Nov-23	114						
O2_CS_RB0740	Female Changing Room (R-R16) - floor finish (Tiling Works)	8	01-Nov-23*	08-Nov-23	109						
O2_CS_RB0750	Acc. Toilet (R-R17) - Remaining floor finish (Tiling Works)	8	01-Nov-23*	08-Nov-23	109						
O2_CS_RB0770	Corridor (R-R02) - Floor Screeding	5	13-Oct-23*	17-Oct-23	131						
O2_CS_RB0780	Corridor (R-R02) next to Conference Room - Sliding window GD8/1	17	15-Dec-23*	31-Dec-23	56						
O2_CS_RB0790	Corridor (R-R02) next to Conference Room - Glass door GD7/1A	17	15-Dec-23*	31-Dec-23	56						
O2_CS_RB0800	Corridor (R-R02) next to Outdoor Wood Decking - Glass door GD9/1	17	15-Dec-23*	31-Dec-23	56						
O2_CS_RB0810	Corridor (R-R02) next to Outdoor Wood Decking - Sliding folding glass door GD4/1	17	15-Dec-23*	31-Dec-23	56						
O2_CS_RB0820	Corridor (R-R02) next to Outdoor Wood Decking - Fixed glass panel GD3/1	17	15-Dec-23*	31-Dec-23	56						
O2_CS_RB0830	Conference Room (R-R03) - Sliding folding door	5	26-Nov-23*	30-Nov-23	87						
O2_CS_RB0840	Conference Room (R-R03) - Raised floor	16	10-Nov-23*	25-Nov-23	92						
O2_CS_RB0850	LAN/ Server Room (R-R07) - Raised floor	16	10-Nov-23*	25-Nov-23	92						
O2_CS_RB0860	Office (R-R05) - Raised floor	19	09-Oct-23*	27-Oct-23	121						
O2_CS_RB0870	Equipment Storage (R-R10) - Wall finish	4	28-Oct-23*	31-Oct-23	117						
O2_CS_RB0880	MCC1 (R-R23) - Remaining raised floor	11	01-Nov-23*	11-Nov-23	106						
O2_CS_RB0890	MCC1 (R-R23) - Wall finish	4	12-Nov-23*	15-Nov-23	102						
O2_CS_RB0900	A/C Room (R-R25) - Remaining raised floor	11	01-Nov-23*	11-Nov-23	106						
O2_CS_RB0910	A/C Room (R-R25) - Wall finish	4	12-Nov-23*	15-Nov-23	102						
O2_CS_RB0920	MCC2 (R-R24) - Remaining raised floor	11	01-Nov-23*	11-Nov-23	106						
O2_CS_RB0930	Irrigation Plant Room (R-R26) - Floor paint	8	16-Nov-23*	23-Nov-23	94						
O2_CS_RB0940	EL Room (for future provision) (R-R27) - Floor paint	8	16-Nov-23*	23-Nov-23	94						
O2_CS_RB0950	FS & Spr. Pump Room (R-R30) - Floor paint	8	16-Nov-23*	23-Nov-23	94						
O2_CS_RB0960	Service Corridor (R-R28) - Floor paint	8	16-Nov-23*	23-Nov-23	94						
O2_CS_RB0970	Fireman's Lift Lobby 1 (R-R29) - Floor (Tiling Works)	4	08-Nov-23*	11-Nov-23	106						
O2_CS_RB0980	Fireman's Lift Lobby 1 (R-R29) - Wall	7	24-Nov-23*	30-Nov-23	87						
O2_CS_RB0990	Protected Lobby (R-32) - Floor paint	7	24-Nov-23*	30-Nov-23	87						
O2_CS_RB1000	Genset Room (R-R31) - Floor paint	7	24-Nov-23*	30-Nov-23	87						
O2_CS_RB1060	Outdoor Wood Decking (R-R33) - Wood deck	13	04-Dec-23*	16-Dec-23	71						
O2_CS_RB1070	Outdoor Wood Decking (R-R33) - Floor Screeding	6	27-Nov-23*	02-Dec-23	85						
O2_CS_RB1080	Outdoor Wood Decking (R-R33) - Waterproof	3	25-Nov-23*	27-Nov-23	90						
O2_CS_RB1090	Wood Deck (R-R36) - Wood deck	13	04-Dec-23*	16-Dec-23	71						
O2_CS_RB1100	Wood Deck (R-R36) - Baffle ceiling	9	22-Nov-23*	30-Nov-23	87						
O2_CS_RB1110	Operator Meeting Room (R-R42) - Raised floor	5	26-Nov-23*	30-Nov-23	87						
O2_CS_RB1120	Store (R-R41) - Floor paint	6	01-Dec-23*	06-Dec-23	81						
O2_CS_RB1130	Store (R-R38) - Floor paint	6	01-Dec-23*	06-Dec-23	81						
O2_CS_RB1140	Skylight (R-R35) - Remaining works of Skylight + Water test	17	30-Oct-23*	15-Nov-23	102						
O2_CS_RB1150	Gridline S6/SD-SF - Baffle ceiling	9	22-Nov-23*	30-Nov-23	92						
O2_CS_RB1160	Fireman's Lift Lobby 1 - Wall	7	06-Dec-23*	12-Dec-23	78						
O2_CS_RB1170	Fireman's Lift Lobby 1 - Floor (Tiling Works)	4	12-Nov-23*	15-Nov-23	102						
O2_CS_RB1180	Fireman's Lift Lobby 2 - Wall	7	06-Dec-23*	12-Dec-23	78						
O2_CS_RB1190	Fireman's Lift Lobby 2 - Floor	4	15-Nov-23*	18-Nov-23	99						
Upper Roof Floor											
O2_CS_RB1200	Fireman's Lift Lobby 1 - Wall	7	06-Dec-23*	12-Dec-23	75						
O2_CS_RB1210	Fireman's Lift Lobby 1 - Floor	5	18-Nov-23*	22-Nov-23	95						
O2_CS_RB1220	Fireman's Lift Lobby 2 - Wall	7	06-Dec-23*	12-Dec-23	75						
O2_CS_RB1230	Fireman's Lift Lobby 2 - Floor	4	22-Nov-23*	25-Nov-23	92						
O2_CS_RB1240	Light Well - 4 nos. Light tube	8	30-Oct-23*	06-Nov-23	111						
O2_CS_RB1250	Wood Deck (R-U03) - Wood deck	13	20-Nov-23*	02-Dec-23	85						
O2_CS_RB1260	R-ST5 - Wood deck	13	04-Dec-23*	16-Dec-23	71						
Stairs											
O2_CS_RB1270	R-ST1 - Floor finish + surface channel	3	26-Oct-23*	28-Oct-23	120						
O2_CS_RB1280	R-ST2 - Floor finish + surface channel	3	26-Oct-23*	28-Oct-23	120						
O2_CS_RB1290	R-ST3 - Floor finish (Grano)	8	14-Nov-23*	21-Nov-23	96						
O2_CS_RB1300	R-ST4 - Floor finish (Grano) + surface channel	8	21-Nov-23*	28-Nov-23	89						
GRANULATION BUILDING & FACILITIES											
ABWF WORKS											
Basement											
O2_CS_GB0010	U/G Tanks - Defects rectification	27	16-Oct-23*	11-Nov-23	106						
O2_CS_GB0020	Pump Pit (G-B01) - Floor finish	6	30-Oct-23*	04-Nov-23	113						
O2_CS_GB0030	Pump Pit (G-B01) - Floor paint	5	13-Nov-23*	17-Nov-23	100						
Ground Floor											
O2_CS_GB0050	Plant Rooms/ Granulation Hall/ WWTP - Floor finish	14	17-Nov-23*	30-Nov-23	87						
O2_CS_GB0060	Plant Rooms - Wall	14	17-Nov-23*	30-Nov-23	87						
O2_CS_GB0070	Granulation Hall - Wall	14	17-Nov-23*	30-Nov-23	87						
O2_CS_GB0080	WWTP - Wall	14	17-Nov-23*	30-Nov-23	87						
O2_CS_GB0090	Air Blower Room - Wall (plastering + Painting)	9	13-Oct-23*	21-Oct-23	127						



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23

- Remaining Work
- Remaining Work (Critical)
- Actual Work
- Level of Effort
- ◆ Baseline Milestone
- ◆ Start Milestone
- ◆ Finish Milestone

Contract No. EP/SP/86/15
Organic Waste Treatment Facilities, Phase 2
3 Months Rolling Programme

extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023			
						Sep	Oct	Nov	Dec
O2_CS_GB0100	Drive Way (G-G02) - Floor screeding	20	16-Oct-23*	04-Nov-23	113				
O2_CS_GB0110	Drive Way (G-G02) - Hardener	8	05-Nov-23*	13-Nov-23	105				
O2_CS_GB0120	Drive Way (G-G02) - Surface channel	16	13-Oct-23*	29-Oct-23	120				
O2_CS_GB0130	Drive Way (G-G02) - Alum. Feature	17	15-Dec-23*	01-Jan-24	56				
O2_CS_GB0140	Male/ Female Changing Room (G-G18, 19, 19a, 20) - Floor finish (Tiling Works)	12	24-Oct-23*	04-Nov-23	113				
O2_CS_GB0150	Male/ Female Changing Room (G-G18, 19, 19a, 20) - Wall (Furring + Tiling Works)	12	24-Oct-23*	04-Nov-23	113				
O2_CS_GB0160	Male/ Female Changing Room (G-G18, 19, 19a, 20) - Ceiling finish	11	05-Nov-23*	15-Nov-23	102				
O2_CS_GB0170	Male/ Female Changing Room (G-G18, 19, 19a, 20) - Toilet cubicle	17	15-Dec-23*	31-Dec-23	56				
O2_CS_GB0180	Staff Resting Area (G-G21A) - Window W06	4	11-Oct-23*	14-Oct-23	134				
O2_CS_GB0190	Staff Resting Area (G-G21A) - Floor Finishes (Tiling Works)	12	24-Oct-23*	04-Nov-23	113				
O2_CS_GB0200	Staff Resting Area (G-G21A) - Wall (Painting)	8	05-Nov-23*	12-Nov-23	105				
O2_CS_GB0210	Workshop (G-G14) - Floor finish (Hardener)	8	05-Nov-23*	12-Nov-23	105				
O2_CS_GB0220	Workshop (G-G14) - Floor paint	8	05-Nov-23*	12-Nov-23	105				
O2_CS_GB0230	Corridor (G-G20) - Floor paint	8	05-Nov-23*	12-Nov-23	105				
O2_CS_GB0240	Lift Lobby (G-G21) - Floor paint	8	13-Nov-23*	20-Nov-23	97				
O2_CS_GB0250	CEMS Room (G-G31) - Floor finish (Epoxy)	8	13-Nov-23*	20-Nov-23	97				
O2_CS_GB0260	CEMS Room (G-G31) - Floor paint	8	13-Nov-23*	20-Nov-23	97				
O2_CS_GB0270	CEMS Room (G-G31) - Wall finish	8	13-Nov-23*	20-Nov-23	97				
O2_CS_GB0280	Pipe Duct Room (G-G12) - Guard railing	8	21-Nov-23*	28-Nov-23	89				
O2_CS_GB0290	EL Room (G-G22) - Floor Finishes (Epoxy)	8	13-Nov-23*	20-Nov-23	97				
O2_CS_GB0300	EL Room (G-G22) - Floor paint	8	13-Nov-23*	20-Nov-23	97				
Mezzanine Floor									
O2_CS_GB0310	Plant Rooms - Floor paint	5	21-Nov-23*	25-Nov-23	92				
O2_CS_GB0320	Plant Rooms - Railing	10	21-Nov-23*	30-Nov-23	87				
O2_CS_GB0330	Flat Roof @+41.725 - Waterproofing	4	01-Dec-23*	04-Dec-23	83				
O2_CS_GB0340	Flat Roof @+41.725 - Floor screeding	4	05-Dec-23*	08-Dec-23	79				
O2_CS_GB0380	Male/ Female Lav. (G-M06, 07, 8 09) - Floor Finishes (Tiling Works)	11	04-Nov-23*	14-Nov-23	103				
O2_CS_GB0390	Male/ Female Lav. (G-M06, 07, 8 09) - Wall (Furring + Tiling Works)	11	04-Nov-23*	14-Nov-23	103				
O2_CS_GB0400	Male/ Female Lav. (G-M06, 07, 8 09) - Ceiling finish	8	16-Nov-23*	23-Nov-23	94				
O2_CS_GB0410	Inspection Corridor (G-M03) - Wall finish (Plastering + Painting)	20	09-Oct-23*	28-Oct-23	120				
O2_CS_GB0420	Inspection Corridor (G-M03) - Floor finish (Tiling Works)	8	24-Oct-23*	31-Oct-23	117				
O2_CS_GB0430	Inspection Corridor (G-M03A) - Wall finish (Plastering + Painting)	20	09-Oct-23*	28-Oct-23	120				
O2_CS_GB0440	Inspection Corridor (G-M03A) - Floor finish (Tiling Works)	8	24-Oct-23*	31-Oct-23	117				
O2_CS_GB0460	Customer LV Switch Room (G-M04) - Remaining raised floor	14	07-Nov-23*	20-Nov-23	97				
O2_CS_GB0470	Customer LV Switch Room (G-M04) - access stairway	11	01-Dec-23*	11-Dec-23	76				
O2_CS_GB0490	Customer LV Switch Room (G-M04) - Guard railing	11	01-Dec-23*	11-Dec-23	76				
O2_CS_GB0500	Customer LV Switch Room (G-M04) - Removable railing to MD6/1	11	01-Dec-23*	11-Dec-23	76				
O2_CS_GB0520	Corridor (G-M19) - Window W07	8	15-Nov-23*	22-Nov-23	95				
O2_CS_GB0530	Corridor (G-M19) - Floor finish (Epoxy)	8	26-Nov-23*	03-Dec-23	84				
O2_CS_GB0540	Corridor (G-M19) - Floor paint	8	26-Nov-23*	03-Dec-23	84				
O2_CS_GB0550	G-ST3 - Floor finish (Epoxy)	8	26-Nov-23*	03-Dec-23	84				
O2_CS_GB0560	G-ST3 - Floor paint	8	26-Nov-23*	03-Dec-23	84				
O2_CS_GB0570	G-ST3 - Wall finish (painting)	8	26-Nov-23*	03-Dec-23	84				
O2_CS_GB0590	Lift Lobby (G-M10) - Floor finish (Tiling Works)	8	24-Oct-23*	31-Oct-23	117				
O2_CS_GB0600	EL Room (G-M12) - Floor paint	8	26-Nov-23*	03-Dec-23	84				
Roof Floor									
O2_CS_GB0610	MCC5, MCC6, MCC7 - Remaining raised floor	4	12-Dec-23*	15-Dec-23	72				
O2_CS_GB0620	MCC5, MCC6, MCC7 - access stairway	4	04-Dec-23*	07-Dec-23	80				
O2_CS_GB0630	Chiller Plant & Pump Room (G-R08) - Floor finish (Epoxy)	4	01-Nov-23*	04-Nov-23	113				
O2_CS_GB0640	Chiller Plant & Pump Room (G-R08) - Grouting to louve surround	4	01-Nov-23*	04-Nov-23	113				
O2_CS_GB0650	RO Room (G-R01) - Wall finish around louve (defect)	4	28-Oct-23*	31-Oct-23	117				
O2_CS_GB0680	Flat Roof @51.250 - Waterproofing	8	01-Nov-23*	08-Nov-23	109				
O2_CS_GB0690	Flat Roof @51.250 - Floor Screeding	12	09-Nov-23*	20-Nov-23	97				
O2_CS_GB0700	Flat Roof @51.250 - Metal fence	4	12-Dec-23*	15-Dec-23	72				
O2_CS_GB0730	EL Room (G-R13) - Floor paint	13	06-Nov-23*	18-Nov-23	99				
Upper Roof Floor									
O2_CS_GB0750	Green Roof - Wood deck	13	06-Nov-23*	18-Nov-23	99				
STATUTORY INSPECTION (FSD, WA, EMSD)									
FIRE SERVICES - FSD									
O2_EM8460	Issuance of F.S. Certificate (Clause 2.4.13, Specs A)	0		20-Sep-23	6				
NGI - EMSD									
O2_EM8530	Application for Approval of Use of NGI - Gas Hddr (Form 105) (Clause 2.4.13, Specs A)	7	14-Sep-23	20-Sep-23	3				
O2_EM8540	EMSD Inspection - Gas Holders	3	21-Sep-23	23-Sep-23	3				
O2_EM8550	Approval of Form 105 - Gas Holder	7	24-Sep-23	30-Sep-23	3				
O2_EM8570	Application for Approval of Use of Balance of NGIs (Form 105) (Clause 2.4.13, Specs A)	7	14-Sep-23	20-Sep-23	0				
O2_EM8580	EMSD Inspection - Balance of NGIs	6	21-Sep-23	26-Sep-23	0				
O2_EM8590	Approval of Form 105 - Balance of NGIs	7	27-Sep-23	03-Oct-23	0				



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23
 Page 3 of 6

- Remaining Work
- Remaining Work (Critical)
- Actual Work
- Level of Effort
- ◆ Baseline Milestone
- ◆ Start Milestone
- ◆ Finish Milestone

**Contract No. EP/SP/86/15
 Organic Waste Treatment Facilities, Phase 2
 3 Months Rolling Programme**

extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023			
						Sep	Oct	Nov	Dec
STREAMLINED T&C SCHEDULE						Sep 50	Oct 51	Nov 52	Dec 53
KEY MILESTONES									
O2_SPA 00020	SPA Streamline Plant Availability Complete	0		31-Dec-23	0				
O2_SPA 00040	FPA Full Plant Availability Complete	0		25-Feb-24	0				
Streamlined Plant Availability (SPA) T&C									
E&M Readiness for SPA									
O2_SPA 00150	24 - Heat Recovery - MC	0	06-Sep-23*		0	06-Sep-23*			
O2_SPA 00165	26 - Waste Water Treatment - MC	0	01-Sep-23*		6	01-Sep-23*			
SPA (Streamline Plant Availability)									
SPA - INSPECTION & PRE-COMMISSIONING									
20 - Waste Reception									
O2_SPA 01310	20 - Waste Reception CRI	7	04-Sep-23	10-Sep-23	2	10-Sep-23			
O2_SPA 01320	20 - Waste Reception RFCC Issued	0		10-Sep-23	2	10-Sep-23			
21 - Anaerobic Digestion									
O2_SPA 01410	21 - Anaerobic Digestion CRI	7	09-Sep-23	15-Sep-23	0	15-Sep-23			
O2_SPA 01420	21 - Anaerobic Digestion RFCC Issued	0		15-Sep-23	0	15-Sep-23			
23 - CHP									
O2_SPA 01510	23 - CHP CRI	7	02-Sep-23	08-Sep-23	0	08-Sep-23			
O2_SPA 01520	23 - CHP RFCC Issued	0		08-Sep-23	0	08-Sep-23			
24 - Heat Recovery									
O2_SPA 01600	24 - Sub-System Inspection & Pre-Commissioning	12	06-Sep-23	17-Sep-23	0	17-Sep-23			
O2_SPA 01610	24 - Heat Recovery CRI	3	18-Sep-23	20-Sep-23	0	20-Sep-23			
O2_SPA 01620	24 - Heat Recovery RFCC Issued	0		20-Sep-23	0	20-Sep-23			
25 - CAPCS									
O2_SPA 01710	25 - CAPCS CRI	7	05-Sep-23	11-Sep-23	1	11-Sep-23			
O2_SPA 01720	25 - CAPCS RFCC Issued	0		11-Sep-23	1	11-Sep-23			
26 - Waste Water Treatment									
O2_SPA 01800	26 - Sub-System Inspection & Pre-Commissioning	30	06-Sep-23	05-Oct-23	1	05-Oct-23			
O2_SPA 01810	26 - Waste Water Treatment CRI	7	06-Oct-23	12-Oct-23	1	12-Oct-23			
O2_SPA 01820	26 - Waste Water Treatment RFCC Issued	0		12-Oct-23	1	12-Oct-23			
27 - SCADA / Control System									
O2_SPA 01910	27 - SCADA / Control System CRI	7	10-Sep-23	16-Sep-23	0	16-Sep-23			
O2_SPA 01920	27 - SCADA / Control System RFCC Issued	0		16-Sep-23	0	16-Sep-23			
SPA - COMMISSIONING									
10 - Utility Electrical									
O2_SPA 02120	10 - Utility Electrical - SURI	7	03-Sep-23	09-Sep-23	3	09-Sep-23			
O2_SPA 02130	10 - Utility Electrical - RFSC	0		09-Sep-23	3	09-Sep-23			
11 - Utility Process									
O2_SPA 02220	11 - Utility Process - SURI	7	05-Sep-23	11-Sep-23	1	11-Sep-23			
O2_SPA 02230	11 - Utility Process - RFSC	0		11-Sep-23	1	11-Sep-23			
Anaerobic Digestion Seeding & Feeding									
O2_SPA 02300	21 - Anaerobic Digestion System Checks (AD Tank 3 & 4)	14	16-Sep-23	29-Sep-23	0	29-Sep-23			
O2_SPA 02310	24 - Heat Recovery System Checks	7	21-Sep-23	27-Sep-23	0	27-Sep-23			
O2_SPA 02320	Anaerobic Digestion Seeding & Feeding (AD Tank 3 & 4) - PSSR	3	28-Sep-23	30-Sep-23	0	30-Sep-23			
O2_SPA 02330	Anaerobic Digestion Seeding & Feeding (AD Tank 3 & 4) - SURI	3	01-Oct-23	03-Oct-23	0	03-Oct-23			
O2_SPA 02340	Anaerobic Digestion Seeding & Feeding (AD Tank 3 & 4) - RFSC	0		03-Oct-23	0	03-Oct-23			
Waste Introduction									
O2_SPA 02400	20 - Waste Reception System Checks (Bunker Tank 1 & 2)	30	12-Sep-23	11-Oct-23	1	11-Oct-23			
O2_SPA 02410	25 - CAPCS System Checks	30	12-Sep-23	11-Oct-23	1	11-Oct-23			
O2_SPA 02420	Waste Introduction - PSSR	15	04-Oct-23	18-Oct-23	1	18-Oct-23			
O2_SPA 02430	Waste Introduction - SURI	7	12-Oct-23	18-Oct-23	1	18-Oct-23			
O2_SPA 02440	Waste Introduction - RFSC	0		18-Oct-23	1	18-Oct-23			
CHP Start-Up Checks (No Grid Connection)									
O2_SPA 02500	23 - CHP System Checks (CHP 1)	15	09-Sep-23	23-Sep-23	0	23-Sep-23			
O2_SPA 02510	23 - CHP - PSSR	12	13-Sep-23	24-Sep-23	6	24-Sep-23			
O2_SPA 02520	23 - CHP - SURI	7	24-Sep-23	30-Sep-23	0	30-Sep-23			
O2_SPA 02530	23 - CHP - RFSC	0		30-Sep-23	0	30-Sep-23			
Waste Water Treatment									
O2_SPA 02600	26 - Waste Water Treatment System Checks (No Anammox)	30	13-Oct-23	11-Nov-23	1	11-Nov-23			
O2_SPA 02610	26 - Waste Water Treatment - PSSR	20	30-Oct-23	18-Nov-23	1	18-Nov-23			
O2_SPA 02620	26 - Waste Water Treatment - SURI	7	19-Nov-23	25-Nov-23	1	25-Nov-23			
O2_SPA 02630	26 - Waste Water Treatment - RFSC	0		25-Nov-23	1	25-Nov-23			
SCADA / Control System									
O2_SPA 02800	27 - SCADA / Control System Checks	14	17-Sep-23	30-Sep-23	0	30-Sep-23			
O2_SPA 02810	27 - SCADA / Control System - PSSR	7	24-Sep-23	30-Sep-23	0	30-Sep-23			
O2_SPA 02820	27 - SCADA / Control System - SURI	3	01-Oct-23	03-Oct-23	0	03-Oct-23			
O2_SPA 02830	27 - SCADA / Control System - RFSC	0		03-Oct-23	0	03-Oct-23			



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23
 Page 4 of 6

Legend:

- Remaining Work
- Remaining Work (Critical)
- Actual Work
- Level of Effort
- Baseline Milestone
- Start Milestone
- Finish Milestone

Contract No. EP/SP/86/15
Organic Waste Treatment Facilities, Phase 2
3 Months Rolling Programme

extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023				
						Sep	Oct	Nov	Dec	
SPA - START-UP										
O2_SPA 03000	Anaerobic Digestion Seeding & Feeding	28	04-Oct-23	31-Oct-23	0					
O2_SPA 03100	Waste Introduction (upto 75T per Day)	65	20-Oct-23	23-Dec-23	0					
O2_SPA 03200	Pig Manure Introduction	30	20-Nov-23*	19-Dec-23	4					
O2_SPA 03300	CHP Start-Up using Bio-Gas - (GCA Testing)	14	17-Dec-23	30-Dec-23	0					
O2_SPA 03400	WWTP Start-Up	30	26-Nov-23	25-Dec-23	1					
SPA - PLANT OPTIMISATION & TESTING										
O2_SPA 04000	Performance Test - 75T Food Waste per Day	3	24-Dec-23	26-Dec-23	0					
O2_SPA 04100	Issue Ready for Operation Certificate (RFOC)	0	27-Dec-23		0					
O2_SPA 04200	Plant Commissioning Report Issued to IC	2	27-Dec-23	28-Dec-23	0					
O2_SPA 04300	Plant Commissioning Report Certified by IC	2	29-Dec-23	30-Dec-23	0					
O2_SPA 04400	Issuance of SPA Certificate of Substantial Completion	1	31-Dec-23	31-Dec-23	0					
Full Plant Availability (FPA) T&C										
E&M Readiness for FPA										
O2_FPA 00100	10 - Utility Electrical SPA - MC	0	31-Aug-23*		26-23*					
O2_FPA 00120	11 - Utility Process - MC	0	31-Aug-23*		46-23*					
O2_FPA 00140	20 - Waste Reception - MC	0	31-Aug-23*		88-23*					
O2_FPA 00160	21 - Anaerobic Digestion - MC	0	31-Aug-23*		0-23*					
O2_FPA 00180	22 - Digestate Treatment - MC	0	20-Sep-23		6					
O2_FPA 00200	23 - CHP - MC	0	31-Aug-23*		31-23*					
FPA (Full Plant Availability)										
FPA - INSPECTION & PRE-COMMISSIONING										
10 - Utility Electrical										
O2_FPA 01100	10 - Sub-System Inspection & Pre-Commissioning	45	10-Sep-23	24-Oct-23	16					
O2_FPA 01120	10 - Utility Electrical CRI	7	25-Oct-23	31-Oct-23	16					
O2_FPA 01140	10 - Utility Electrical RFCC Issued	0		31-Oct-23	16					
11 - Utility Process										
O2_FPA 01200	11 - Sub-System Inspection & Pre-Commissioning	28	12-Sep-23	09-Oct-23	34					
O2_FPA 01220	11 - Utility Process CRI	7	10-Oct-23	16-Oct-23	34					
O2_FPA 01240	11 - Utility Process RFCC Issued	0		16-Oct-23	34					
20 - Waste Reception										
O2_FPA 01300	20 - Sub-System Inspection & Pre-Commissioning	45	01-Nov-23	15-Dec-23	26					
O2_FPA 01320	20 - Waste Reception CRI	7	16-Dec-23	22-Dec-23	26					
O2_FPA 01340	20 - Waste Reception RFCC Issued	0		22-Dec-23	26					
21 - Anaerobic Digestion										
O2_FPA 01400	21 - Sub-System Inspection & Pre-Commissioning	45	04-Oct-23	17-Nov-23	3					
O2_FPA 01420	21 - Anaerobic Digestion CRI	7	18-Nov-23	24-Nov-23	3					
O2_FPA 01440	21 - Anaerobic Digestion RFCC Issued	0		24-Nov-23	3					
22 - Digestate Treatment (Granulation)										
O2_SPA 01850	22 - Sub-System Inspection & Pre-Commissioning	30	20-Sep-23	19-Oct-23	6					
O2_SPA 01860	22 - Granulation System CRI	7	20-Oct-23	26-Oct-23	6					
O2_SPA 01870	22 - Granulation System RFCC Issued	0		26-Oct-23	6					
23 - CHP										
O2_FPA 01700	23 - Sub-System Inspection & Pre-Commissioning	40	01-Oct-23	09-Nov-23	0					
O2_FPA 01720	23 - CHP CRI	7	10-Nov-23	16-Nov-23	0					
O2_FPA 01740	23 - CHP RFCC Issued	0		16-Nov-23	0					
27 - SCADA / Control System										
O2_FPA 01800	27 - SCADA / Control System Inspection & Pre-Commissioning	30	04-Oct-23	02-Nov-23	7					
O2_FPA 01820	27 - SCADA / Control System CRI	7	03-Nov-23	09-Nov-23	7					
O2_FPA 01840	27 - SCADA / Control System Issued	0		09-Nov-23	7					
FPA - COMMISSIONING										
10 - Utility Electrical										
O2_FPA 02100	10 - Utility Electrical System Checks	24	01-Nov-23	24-Nov-23	20					
O2_FPA 02120	10 - Utility Electrical - PSSR	18	09-Nov-23	26-Nov-23	24					
O2_FPA 02140	10 - Utility Electrical - SURI	6	25-Nov-23	30-Nov-23	20					
O2_FPA 02160	10 - Utility Electrical - RFSC	0		30-Nov-23	20					
11 - Utility Process										
O2_FPA 02200	11 - Utility Process System Checks	24	17-Oct-23	09-Nov-23	34					
O2_FPA 02220	11 - Utility Process - PSSR	18	25-Oct-23	11-Nov-23	39					
O2_FPA 02240	11 - Utility Process - SURI	7	10-Nov-23	16-Nov-23	34					
O2_FPA 02260	11 - Utility Process - RFSC	0		16-Nov-23	34					
20 - Waste Introduction										
O2_FPA 02500	20 - Waste Reception System Checks	24	23-Dec-23	15-Jan-24	26					
O2_FPA 02520	20 - Waste Introduction - PSSR	24	31-Dec-23	23-Jan-24	26					
O2_FPA 02540	20 - Waste Introduction - SURI	7	16-Jan-24	22-Jan-24	27					
O2_FPA 02560	20 - Waste Introduction - RFSC	0		23-Jan-24	26					
21 - Anaerobic Digestion										



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23
 Page 5 of 6

■ Remaining Work
■ Remaining Work (Critical)
■ Actual Work
■ Level of Effort
◆ Baseline Milestone
◆ Start Milestone
◆ Finish Milestone

Contract No. EP/SP/86/15
Organic Waste Treatment Facilities, Phase 2
3 Months Rolling Programme

extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2023			
						Sep	Oct	Nov	Dec
O2_FPA 02600	21 - Anaerobic Digestion System Checks	24	25-Nov-23	18-Dec-23	3				
O2_FPA 02620	21 - Anaerobic Digestion Seeding & Feeding - PSSR	24	02-Dec-23	25-Dec-23	3				
O2_FPA 02640	21 - Anaerobic Digestion Seeding & Feeding - SURI	7	26-Dec-23	01-Jan-24	3				
O2_FPA 02660	21 - Anaerobic Digestion Seeding & Feeding - RFSC	0		01-Jan-24	3				
22 - Digestate Treatment (Granulation)									
O2_FPA 02700	22 - Granulation System Checks	45	27-Oct-23	10-Dec-23	6				
O2_FPA 02720	22 - Granulation System - PSSR	20	28-Nov-23	17-Dec-23	6				
O2_FPA 02740	22 - Granulation System - SURI	7	18-Dec-23	24-Dec-23	6				
O2_FPA 02760	22 - Granulation System - RFSC	0		24-Dec-23	6				
23 - CHP Start-Up for Grid Export Testing									
O2_FPA 02800	23 - CHP System Checks	30	17-Nov-23	16-Dec-23	0				
O2_FPA 02820	23 - CHP - PSSR	30	21-Nov-23	20-Dec-23	0				
O2_FPA 02840	23 - CHP - SURI	7	14-Dec-23	20-Dec-23	0				
O2_FPA 02860	23 - CHP - RFSC	0		20-Dec-23	0				
27 - SCADA / Control System									
O2_FPA 02900	27 - SCADA / Control System Checks	30	10-Nov-23	09-Dec-23	8				
O2_FPA 02920	27 - SCADA / Control System - PSSR	20	15-Nov-23	04-Dec-23	13				
O2_FPA 02940	27 - SCADA / Control System - SURI	3	10-Dec-23	12-Dec-23	8				
O2_FPA 02960	27 - SCADA / Control System - RFSC	0		12-Dec-23	8				
FPA - START-UP									
O2_FPA 03000	CHP Start-Up & Grid Testing	60	21-Dec-23	18-Feb-24	0				
O2_FPA 03100	Waste Water Treatment	45	02-Jan-24	15-Feb-24	3				
O2_FPA 03200	Granulation Start-Up	50	25-Dec-23	12-Feb-24	6				
FPA - PLANT OPTIMISATION & TESTING									
O2_FPA 04000	Performance Test	4	19-Feb-24	22-Feb-24	0				
O2_FPA 04100	Issue Ready for Operation Certificate (RFOC)	0	23-Feb-24		0				
O2_FPA 04200	Plant Commissioning Report Issued	3	23-Feb-24	25-Feb-24	0				
O2_FPA 04300	Completion of FPA	0		25-Feb-24	0				



File Name: WP_07 R4-1
 Layout: ORRC2_WP_07.2023 R4-3M
 TASK filters: W7-3M, W7-3M1, WP7_R4.
 Date Printed: 30-Sep-23

- Remaining Work
- Remaining Work (Critical)
- Actual Work
- Level of Effort
- ◆ Baseline Milestone
- ◆ Start Milestone
- ◆ Finish Milestone



**Contract No. EP/SP/86/15
 Organic Waste Treatment Facilities, Phase 2
 3 Months Rolling Programme**



extracted from WP07			
Date	Revision	Checked	Approved
31-Aug-23			

Appendix E



Graphical Plots of Monitoring Results



Construction Noise

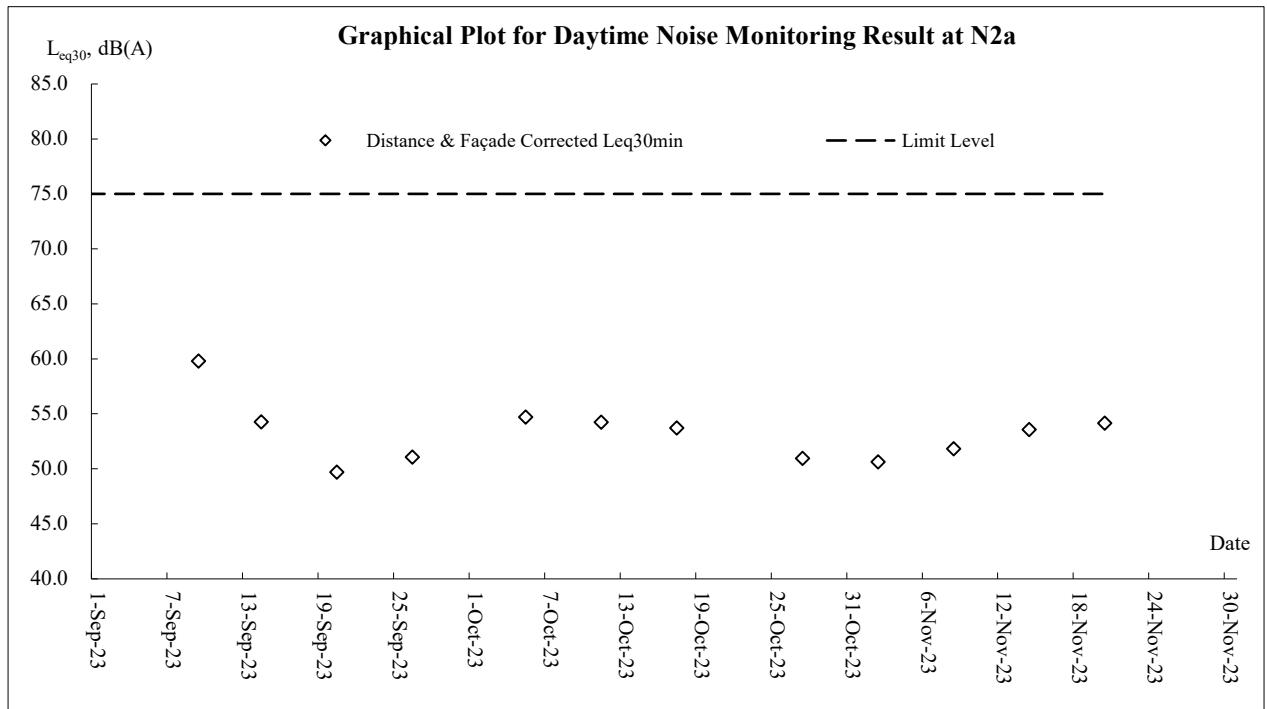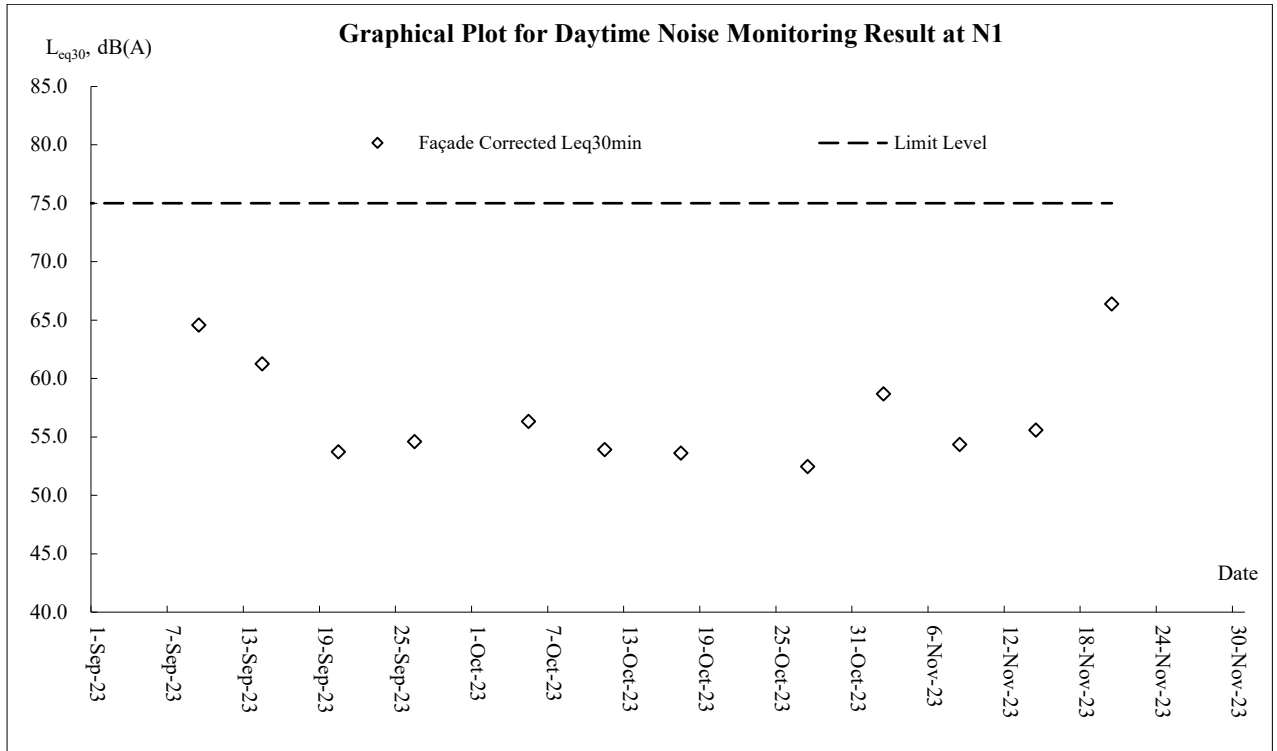

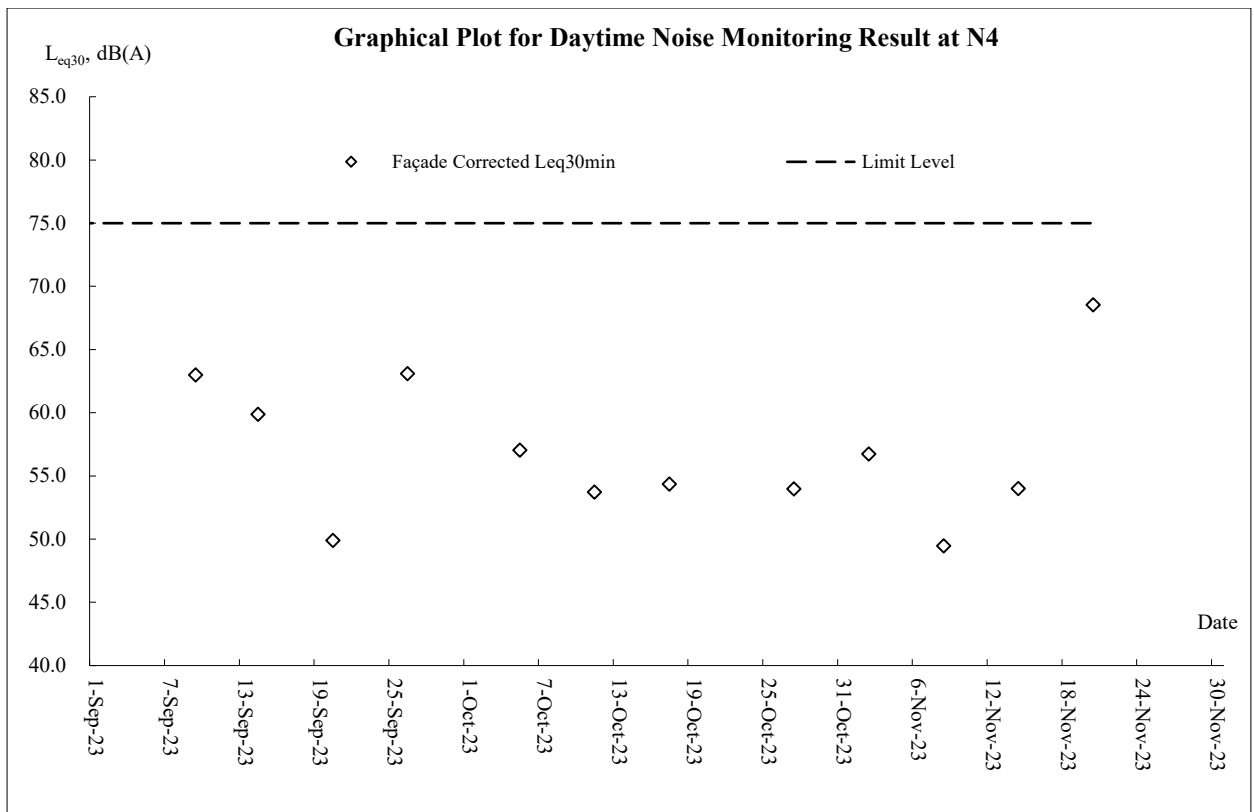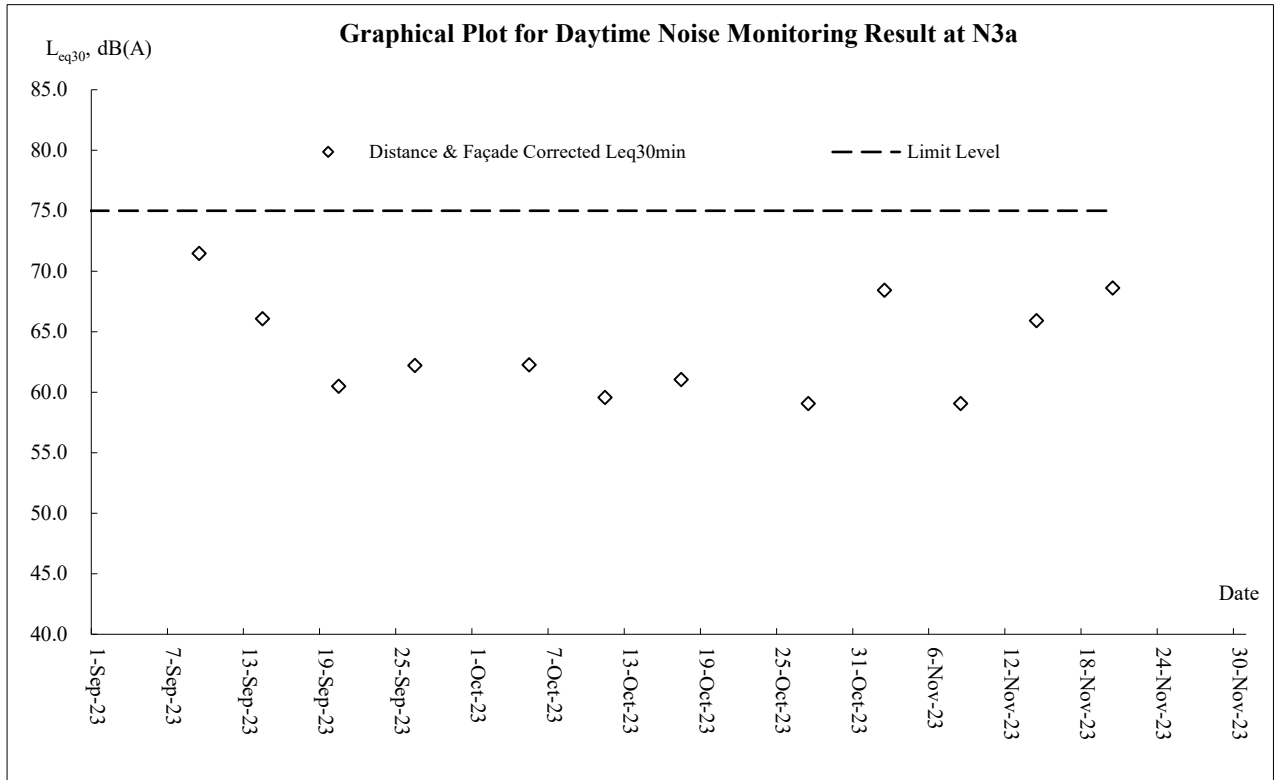

Additional Noise Monitoring

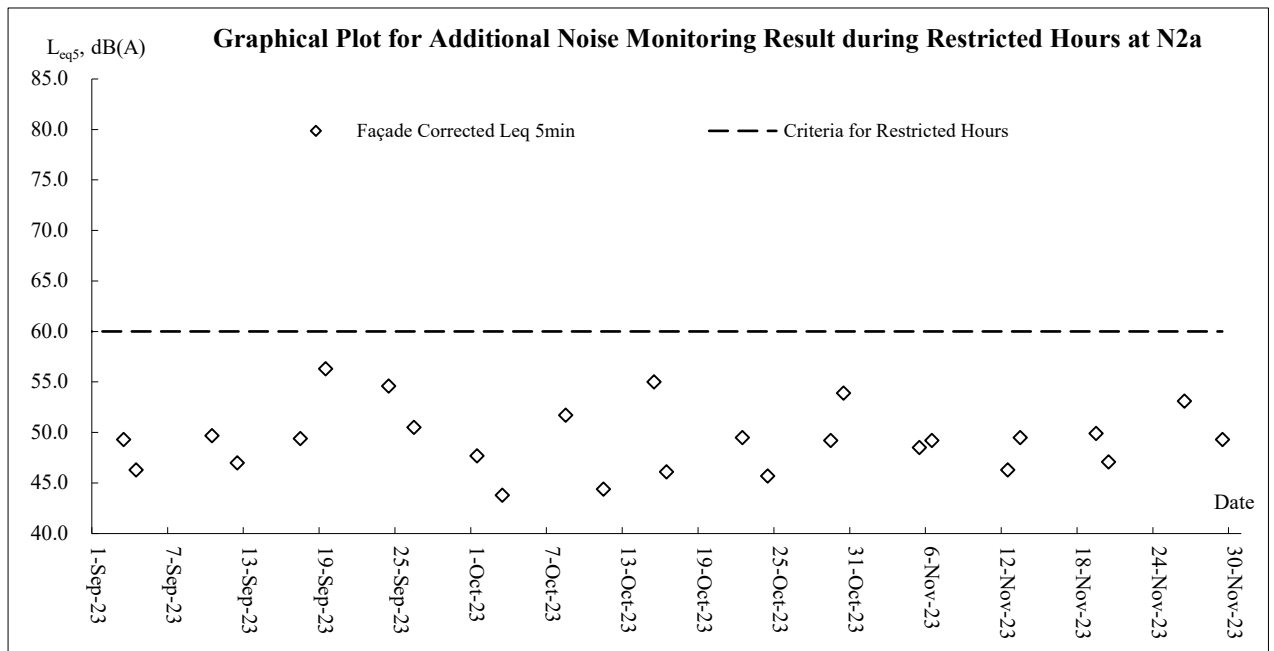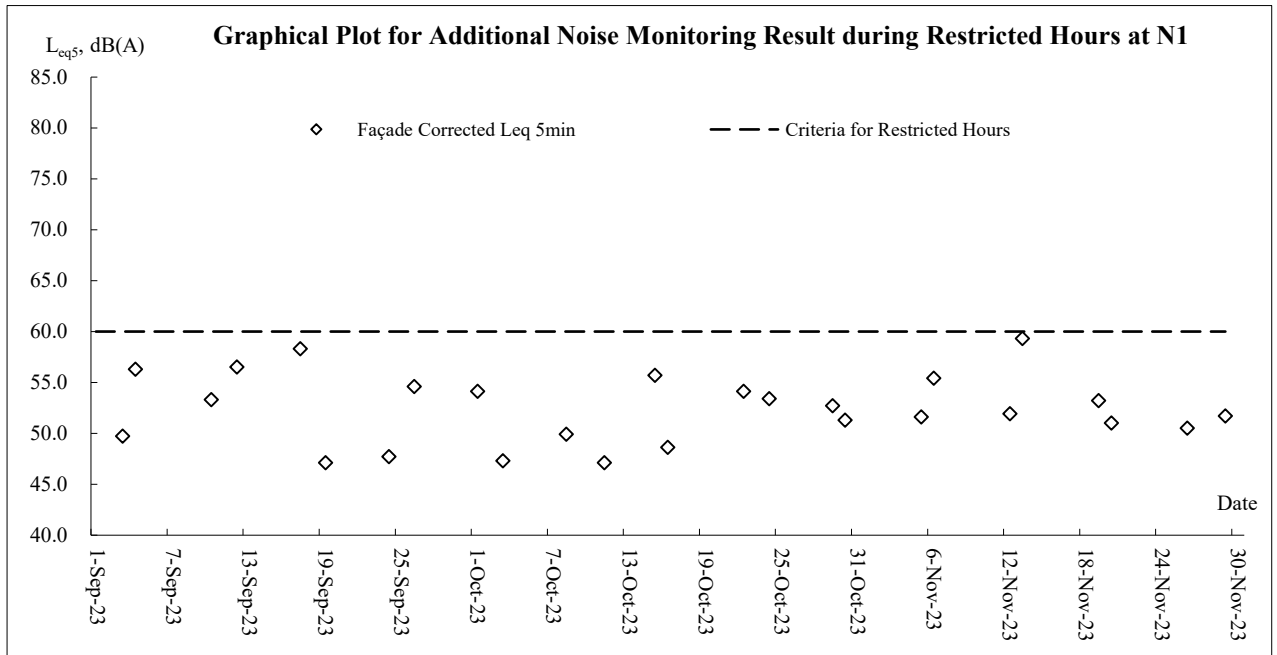

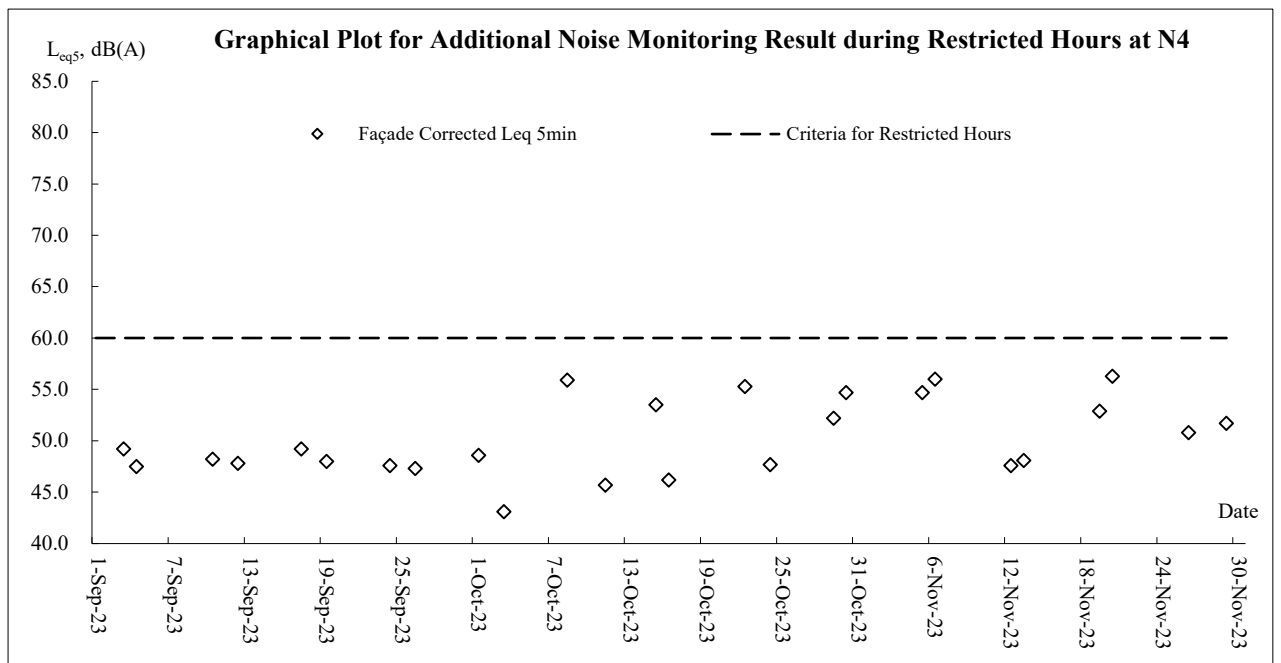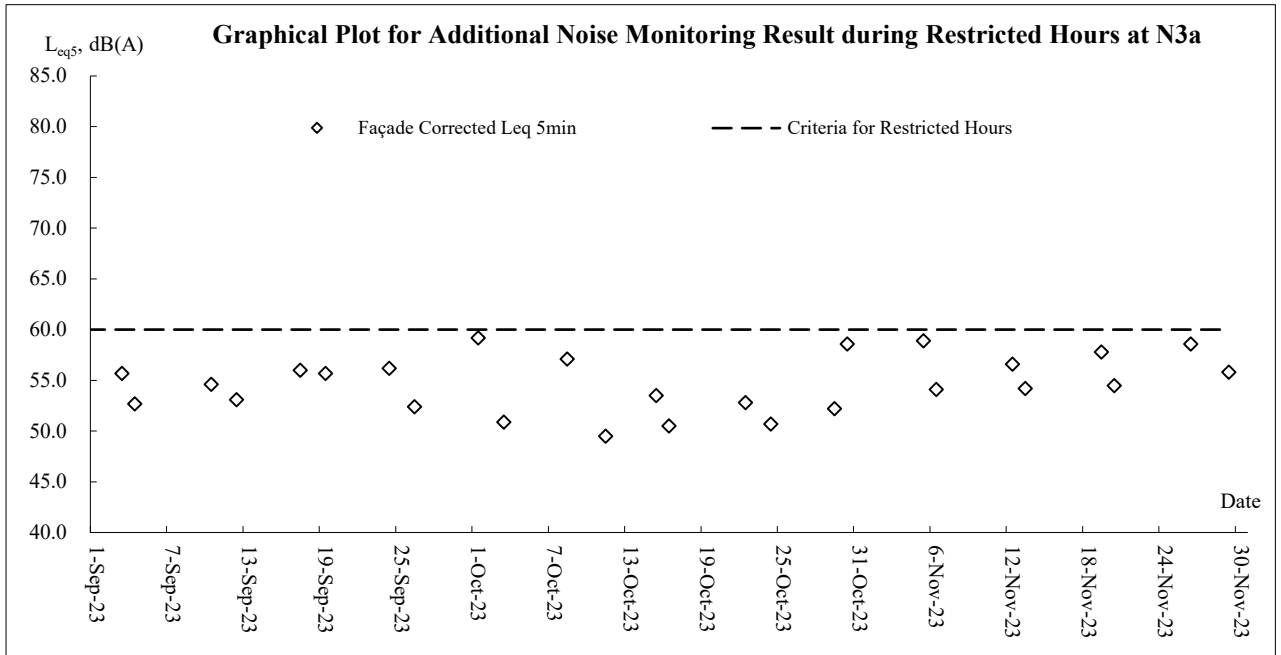

Appendix F

Meteorological Information

The weather of September 2023

In terms of extreme weather, September 2023 was an eventful month in Hong Kong with the ferocious strike by Super Typhoon Saola on 1 – 2 September and the phenomenal rainstorm on 7 – 8 September. With a maximum sustained wind of 230 km/h near its centre, Saola was the second most intense tropical cyclone affecting the South China Sea since 1950 and Hurricane Signal No. 10 was issued in Hong Kong during the passage of Saola, the first time since Super Typhoon Mangkhut hit Hong Kong in September 2018. A trough of low pressure associated with the remnant of tropical cyclone Haikui brought prolonged torrential rain to Hong Kong on 7 – 8 September and necessitated the issuance of the Black Rainstorm Warning for 16 hours and 35 minutes, setting the longest record since the introduction of the rainstorm warning system in 1992. Mainly attributing to the heavy rain associated with Saola and troughs of low pressure in the first half of the month, the Observatory recorded an all-time high September rainfall of 1067.1 millimetres, more than three times of the September normal of 321.4 millimetres and easily breaking the previous record of 844.2 millimetres set way back in September 1952. Moreover, the rainfall deficit in the first eight months of this year was mostly compensated by the record-breaking rainfall in September. The accumulated rainfall this year up to September was 2224.3 millimetres, slightly less than the normal figure of 2242.8 millimetres for the same period. Despite the stormy weather in the first part of the month, there was a long spell of sunny and very hot weather with 10 consecutive very hot days from 21 to 30 September in the later part of the month. It also set the longest record of consecutive very hot days for September. Overall, the month remained hotter than usual with a mean temperature of 28.5 degrees, 0.6 degrees above the normal of 27.9 degrees.

The weather of October 2023

With more than usual moisture in the lower atmosphere over southern China, October 2023 was much cloudier than usual in Hong Kong. The mean amount of cloud in the month was 79 percent, 21 percent above the normal of 58 percent and the second highest on record for October. The duration of bright sunshine in the month was only 138.9 hours, about 30 percent lower than the normal figure of 197.8 hours and the fourth lowest on record for October. Mainly attributing to the record-breaking rainfall associated with tropical cyclone Koinu on 8 – 9 October, the month was also much wetter than usual. The monthly total rainfall was 546.0 millimetres, more than four times of the normal figure of 120.3 millimetres and the fifth highest on record for October. The accumulated rainfall this year up to October was 2770.3 millimetres, about 17 percent more than the normal figure of 2363.1 millimetres for the same period. Despite the below normal sunshine, the month was warmer than usual. The mean temperature of 26.4 degrees was 0.7 degrees above the normal and one of the fourth highest for October on record. There were 3 very hot days in the early part of the month, the highest on record for October.

The weather of November 2023

Under the influence of a dry northeast monsoon, the weather of Hong Kong was fine and dry during the day on the first six days of the month. With plenty of sunshine, temperatures at the Observatory rose to a maximum of 30.7 degrees on the afternoon of 6 November, the highest of the month. Moreover, the daily mean temperature of 27.6 degrees on that day was the highest on record for November.

Appendix G

Waste Flow Table

Monthly Summary Waste Flow Table for 2023

Version: 0

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantity of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects (see Note 10)	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging (see Notes 4)	Plastics (see Notes 2 &4)	Chemical Waste	Others, eg. general refuse
	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m3)
sub-total up to 2022	98.401	0.000	0.000	83.508	14.660	0.233	337.486	1.250	0.700	0.000	3.497
Jan-23	0.314	0.000	0.000	0.000	0.314	0.000	0.000	0.000	0.000	0.000	0.136
Feb-23	0.932	0.000	0.000	0.000	0.932	0.000	0.000	0.000	0.000	0.000	0.059
Mar-23	0.644	0.000	0.000	0.000	0.644	0.000	0.000	0.000	0.000	0.000	0.131
Apr-23	0.633	0.000	0.000	0.000	0.633	0.000	0.000	0.000	0.000	0.000	0.103
May-23	0.779	0.000	0.000	0.000	0.779	0.000	0.000	0.000	0.000	0.000	0.104
Jun-23	0.329	0.000	0.000	0.000	0.329	0.000	0.000	0.000	0.000	0.000	0.113
Sub total (since 2019)	102.032	0.000	0.000	83.508	18.291	0.233	337.486	1.250	0.700	0.000	4.143
Jul-23	0.098	0.000	0.000	0.000	0.098	0.000	0.000	0.100	0.000	0.000	0.207
Aug-23	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.150	0.000	0.000	0.098
Sep-23	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.052
Oct-23	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.057
Nov-23	0.052	0.000	0.000	0.000	0.052	0.000	0.000	0.000	0.000	0.000	0.075
Dec-23											
Total (since 2019)	102.182	0.000	0.000	83.508	18.441	0.233	337.486	1.500	0.700	0.000	4.633

Appendix H

Environmental Mitigation Implementation Schedule
(Extracted from EM&A Manual)

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
Air Quality Impact (Construction)									
3.8.1.1	2.4	<p>General Dust Control Measures</p> <p>Dust emissions could be suppressed by regular water spraying on site. In general, water spraying twice a day could reduce dust emission from active construction area by 50%. However, for the Project more frequent water spraying is proposed. Watering eight times per day, or once every 1.5 hours, is suggested at all active works areas in order to achieve a higher dust suppression efficiency of 87.5%.</p>	Within construction site / Duration of the construction phase	Contractor		✓			EIA Recommendation and Air Pollution Control (Construction Dust) Regulation
3.8.1.2	2.4	<p>Best Practice For Dust Control</p> <p>The relevant best practices for dust control as stipulated in the <i>Air Pollution Control (construction Dust) Regulation</i> should be adopted to further reduce the construction dust impacts of the Project. These best practices include:</p> <p><i>Good Site Management</i></p> <ul style="list-style-type: none"> ▪ Good site management is important to help reducing potential air quality impact down to an acceptable level. As a general guide, the Contractor should maintain a high standard of housekeeping to prevent emissions of fugitive dust. Loading, unloading, handling and storage of raw materials, wastes or by-products should be carried out in a manner so as to minimise the release of visible dust emission. Any piles of materials accumulated on or around the work areas should be cleaned up regularly. Cleaning, repair and maintenance of all plant facilities within the work areas should be carried out in a manner minimising generation of fugitive dust emissions. The material should be handled properly to prevent fugitive dust emission before cleaning. <p><i>Disturbed Parts of the Roads</i></p> <ul style="list-style-type: none"> ▪ Each and every main temporary access should be paved with concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials; or ▪ Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road 	Within construction site / Duration of the construction phase	Contractor		✓			EIA Recommendation and Air Pollution Control (Construction Dust) Regulation

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p>surface wet.</p> <p><i>Exposed Earth</i></p> <ul style="list-style-type: none"> Exposed earth should be properly treated by compaction, hydroseeding, vegetation planting or seeding with latex, vinyl, bitumen within six months after the last construction activity on the site or part of the site where the exposed earth lies. <p><i>Loading, Unloading or Transfer of Dusty Materials</i></p> <ul style="list-style-type: none"> All dusty materials should be sprayed with water immediately prior to any loading or transfer operation so as to keep the dusty material wet. <p><i>Debris Handling</i></p> <ul style="list-style-type: none"> Any debris should be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the three sides. Before debris is dumped into a chute, water should be sprayed so that it remains wet when it is dumped. <p><i>Transport of Dusty Materials</i></p> <ul style="list-style-type: none"> Vehicle used for transporting dusty materials/spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards. <p><i>Wheel washing</i></p> <ul style="list-style-type: none"> Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. <p><i>Use of vehicles</i></p> <ul style="list-style-type: none"> The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. Where a vehicle leaving the construction site is carrying a load of dusty materials, the load should be covered entirely 							

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle. <i>Site hoarding</i> <ul style="list-style-type: none"> Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit. 							
Air Quality Impact (Operation)									
3.8.2	2.3	Odour patrol at site boundary of the Project	Site boundary / During operation stage (the need to continue the odour patrol after the end of the 2-year monitoring period would depend on the monitoring results and should be agreed with EPD)	OWTF Operator	✓		✓		EIAO-TM
3.8.2	2.4	Install gas cleaning equipment and stack on the CHP and odour treatment unit <ul style="list-style-type: none"> The preliminary design suggests the use of a two stage process involving either a biofilter or Ultraviolet Light (UV-C) together with ozone treatment as the first stage, and an activated carbon filter as the second stage for the odour treatment unit. It is recommended to install the UV-C and ozone treatment system with second stage active carbon filters as this has a lower footprint requirement than the biofilter option. However, the actual unit installed depends on the final design by the contractor in the design phase. The preliminary design incorporates a combination of thermal and catalytic treatment processes to remove pollutants from the exhaust gasses from the CHP. Both the odour treatment unit and the CHP emissions are suggested to be directed to a flue to aid the dispersion and minimise effects on ASRs. 	CHP and odour treatment unit	Design Consultant / OWTF Operator	✓		✓		EIA Recommendation
Hazard Risk Assessment (Operation)									

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
4.9	3.2	<p>The HA has assumed that the following “Good Practices” and “recommended design measures” for the safe operation of OWTF 2 shall be carried out as far as reasonably practicable:</p> <ul style="list-style-type: none"> ▪ The process plant building will be provided with adequate number of gas detectors distributed over the various areas of potential leak sources to provide adequate coverage. ▪ All electrical equipment inside the building will be classified in accordance with the electrical area classification requirements. No unclassified electrical equipment will be used during operations or maintenance. ▪ Reference can be made to Codes of Practice and guidance issued in Europe that applies to places where explosive atmospheres may occur (called ‘ATEX’ requirements). These are covered as part of the European Directive: the Explosive Atmospheres Directive (99/92/EC) and the UK regulations, Dangerous Substances and Explosive Atmospheres Regulations 2002 (DSEAR). Where potentially explosive atmospheres may occur in the workplace, the requirements include, identifying and classifying (zoning) areas where potentially explosive atmospheres may occur; avoiding ignition sources in zoned areas, in particular those from electrical and mechanical equipment; where necessary, identifying the entrances to zoned areas; providing appropriate anti-static clothing for employees; and before they come into operation, verifying the overall explosion protection safety of areas where explosive atmospheres may occur. ▪ All safety valves design shall take into account discharging any released fluid to a safe location, or stopping misdirection of fluid flows in order to avoid hazardous outcome. ▪ Safety markings and crash barriers will be provided to the aboveground piping, digesters and the gas holder near the entrance. ▪ Lightning protection installations will be installed following IEC 62305, BS EN 62305, AS/NZS 1768, NFPA 780 or equivalent standards. ▪ A 10m high boundary wall with fire resistance will be 	During design and operation phases	Design Consultant / OWTF Operator	✓		✓		EIAO & EIAO TM Annex 4

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p>provided in the vicinity of the digester tanks, gasholders and gas purification equipment to protect the equipment against external fires, and to provide some protection to external areas from the effects of fire/explosion.</p> <ul style="list-style-type: none"> ▪ Suitable fire extinguishers will be provided within the site. An External Water Spray System (EWSS) will be installed in appropriate areas, such as around the gasholders, gas purification, desulphurisation units, and digester areas. The facilities will also be equipped with fire and gas detection system and fire suppression system. Stringent procedures are implemented to prohibit smoking or naked flames to be used on-site. ▪ Fixed crash barriers will be provided in areas where process equipment is adjacent to the internal roadway to protect against vehicle collision. Adequate warning signage and lighting will also be provided and maximum speed limit will also be in place. 							
Noise Impact (Construction)									
5.9.1	4.2.7	<p>Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during each phase of construction:</p> <ul style="list-style-type: none"> ▪ only well-maintained plant to be operated on-site and plant should be serviced regularly during the construction works; ▪ machines and plant that may be in intermittent use to be shut down between work periods or should be throttled down to a minimum; ▪ plant known to emit noise strongly in one direction, should, where possible, be orientated to direct noise away from the NSRs; ▪ mobile plant should be sited as far away from NSRs as possible; and ▪ material stockpiles and other structures to be effectively utilised, where practicable, to screen noise from on-site 	Within construction site / During construction phase	Contractor		✓			EIAO, EIAO-TM and Noise Control Ordinance

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		construction activities.							
5.9.1	4.2.7	Selection of Quieter PME The recommended quieter PME adopted in the assessment were taken from the EPD's QPME Inventory and British Standard, namely <i>Noise Control on Construction and Open Sites, BS 5228: Part 1: 2009</i> . It should be noted that the silenced PME selected for assessment can be found in Hong Kong.	Within construction site / During construction phase	Contractor		✓			EIAO, EIAO-TM and Noise Control Ordinance
5.9.1	4.2.7	Use of Movable Noise Barriers Movable noise barriers can be very effective in screening noise from particular items of plant when constructing the Project. Noise barriers located along the active works area close to the noise generating component of a PME could produce at least 10 dB(A) screening for stationary plant and 5 dB(A) for mobile plant provided the direct line of sight between the PME and the NSRs is blocked.	Within construction site / During construction phase	Contractor		✓			EIAO, EIAO-TM and Noise Control Ordinance
5.9.1	4.2.7	Use of Noise Enclosure/ Acoustic Shed The use of noise enclosure or acoustic shed is to cover stationary PME such as air compressor and generator. With the adoption of the noise enclosure, the PME could be completely screened, and noise reduction of 15 dB(A) can be achieved according to the EIAO Guidance Note No.9/2010.	Within construction site / During construction phase	Contractor		✓			EIAO, EIAO-TM and Noise Control Ordinance
5.9.1	4.2.7	Use of Noise Insulating Fabric Noise insulating fabric can also be adopted for certain PME (e.g. pilling machine etc). The fabric should be lapped such that there are no openings or gaps on the joints. According to the approved Tsim Sha Tsui Station Northern Subway EIA report (AEIAR-127/2008), a noise reduction of 10 dB(A) can be achieved for the PME lapped with the noise insulating fabric.	Within construction site / During construction phase	Contractor		✓			EIAO, EIAO-TM and Noise Control Ordinance
Noise Impact (Operation)									
5.9.2	4.2.7	Fixed Plant Noise Specification of the maximum allowable sound power levels of the proposed fixed plants should be followed. The following noise reduction measures should be considered as far as practicable during operation: <ul style="list-style-type: none"> ▪ Choose quieter plant such as those which have been effectively silenced; 	Within construction site / During operation phase / Throughout operation phase	Design Consultant / Contractor	✓		✓		EIAO, EIAO-TM and Noise Control Ordinance

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<ul style="list-style-type: none"> ▪ Include noise levels specification when ordering new plant (including chillier and E/M equipment); ▪ Locate fixed plant/louver away from any NSRs as far as practicable; ▪ Locate fixed plant in walled plant rooms or in specially designed enclosures; ▪ Locate noisy machines in a completely separate building; ▪ Install direct noise mitigation measures including silencers, acoustic louvers and acoustic enclosure where necessary; and ▪ Develop and implement a regularly scheduled plant maintenance programme so that equipment is properly operated and serviced in order to maintain a controlled level of noise. 							
Water Quality Impact (Construction)									
6.8.1.1	5.3	<p>Construction site runoff</p> <p>The site practices outlined in ProPECC Note PN 1/94 should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. The following measures are recommended to protect water quality and sensitive uses of the coastal area, and when properly implemented should be sufficient to adequately control site discharges so as to avoid water quality impacts:</p> <ul style="list-style-type: none"> ▪ At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels, earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system should be undertaken by the Contractor prior to the commencement of construction; ▪ Sand/silt removal facilities such as sand/silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of efficient silt 	Within construction site / Duration of the construction phase	Contractor		✓			ProPECC Note PN 1/94

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p>removal facilities should be based on the guidelines in Appendix A1 of ProPECC Note PN 1/94. Sizes may vary depending upon the flow rate. The detailed design of the sand/silt traps should be undertaken by the Contractors prior to the commencement of construction.</p> <ul style="list-style-type: none"> ▪ All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. ▪ Measures should be taken to minimize the ingress of site drainage into excavations. If excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities. ▪ All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facility should be provided at construction site exit where practicable. Wash-water should have sand and silt settled out and removed regularly to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. ▪ Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. ▪ Manholes (including newly constructed ones) should be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and stormwater runoff being directed into 							

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		foul sewers. <ul style="list-style-type: none"> Precautions should be taken at any time of the year when rainstorms are likely. Actions should be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC Note PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. Bentonite slurries used in piling or slurry walling should be reconditioned and reused wherever practicable. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after all the related construction activities are completed. The requirements in ProPECC Note PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 							
6.8.1.2	5.3	General construction activities Construction solid waste, debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby storm water drain. Stockpiles of cement and other construction materials should be kept covered when not being used.	Within construction site / During construction phase	Contractor		✓			ProPECC Note PN 1/94
6.8.1.3	5.3	Excavation works The construction programme should be properly planned to minimise excavation works during the wet season (April to September), temporarily exposed slope/soil surfaces should be covered by a tarpaulin or other means, as far as practicable. Interception channels should be provided (e.g. along the crest/edge of the excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should be in place to ensure that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94.	Within construction site / During construction phase	Contractor		✓			ProPECC Note PN 1/94
6.8.1.4	5.3	Accidental spillage <ul style="list-style-type: none"> The Contractor should register as a chemical waste producer 	Within construction site / During construction phase	Contractor		✓			ProPECC Note PN 1/94 and Waste Disposal

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p>if chemical wastes are produced from construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p> <ul style="list-style-type: none"> ▪ Maintenance of vehicles and equipment, involving activities with potential for leakage and spillage, should only be undertaken within areas appropriately equipped to control these discharges. ▪ Oils and fuels should only be stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to any nearby storm water drain, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event. ▪ Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: <ul style="list-style-type: none"> – Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. – Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. – Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 						Ordinance	
6.8.1.5	5.3	<p>Sewage effluent from construction workforce</p> <p>Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be</p>	Within construction site / During construction phase	Contractor		✓			ProPECC Note PN 1/94

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		responsible for appropriate disposal and maintenance.							
Water Quality Impact (Operation)									
6.8.2.1	5.3	<p>Sewage effluent and sewerage impact</p> <p>In order to minimise the risk of exceeding capacity of the sewerage system, on-site underground storage of effluent is recommended for the OWTF 2, with a capacity of 6 hours of peak flow. Using the values presented in the preliminary design, the on-site storage required to buffer excess capacity would be equivalent to 30 m³. A below ground effluent retention tank would function to store effluent produced during peak periods when usage of the Sha Ling pumping station is high. Effluent stored during such periods could then be pumped out of the retention tank and discharged into the public sewer during off-peak times when capacity is sufficient.</p>	Within construction site / During design and operation phase	Design Consultant / OWTF Operator	✓		✓		EIA recommendations
6.8.2.2	5.3	<p>Wastewater generation from organic waste treatment processes</p> <p>Wastewater must be collected and diverted to the wastewater treatment plant (WWTP).</p> <p>An adequately sized WWTP with technologies such as membrane bioreactor, reverse osmosis or multi-phase separation process or system should be provided for the OWTF 2. Polluting parameters in the effluent should be in compliance with the requirements as specified in the TM-DSS.</p> <p><i>Leachate from the waste reception and composting process</i></p> <ul style="list-style-type: none"> A drainage system will be provided at the reception area connecting to the proposed onsite WWTP. The leachate would be treated in the WWTP and there would be no direct discharge of leachate. <p><i>Dewatering of the digestate from the separators</i></p> <ul style="list-style-type: none"> The wastewater generated from the dewatering of digestate from the digesters is expected to be around 229.18 m³/day and a peak flow of 5.31L/s. The on-site WWTP will deploy suitable treatment process in order to reduce the pollution level to an acceptable standard. The effluent shall be treated according to the TM-DSS standard before discharging to foul sewers. 	Within construction site / During design and operation phase	Design Consultant / OWTF Operator	✓		✓		TM-DSS, Water Pollution Control Ordinance

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p><i>Condensate from biogas drying, odour treatment and ventilation system</i></p> <ul style="list-style-type: none"> Condensate from biogas handling and wastewater from the odour treatment process would be collected and transferred to the WWTP. There is no direct discharge of wastewater to the sewer. <p><i>Washing of waste delivery trucks</i></p> <ul style="list-style-type: none"> Surplus wastewater generated from the vehicle washing facilities would be collected and transferred to the WWTP for further treatment before discharging to the foul sewer. <p><i>Untreated wastewater from wastewater treatment plant</i></p> <ul style="list-style-type: none"> Maintenance of the WWTP and its connection pipe work would be conducted regularly to confirm the condition of the holding tank and pipes. This will ensure early detection of any damage for repair or replacement. <p><i>Leakage of materials from WWTP</i></p> <ul style="list-style-type: none"> Regular scheduled maintenance of the WWTP will be carried out to confirm the condition of the facility and detect any damages at an early stage for repair or replacement. 							
6.8.2.3	5.3	<p>Contaminated stormwater runoff and accidental spillages</p> <p>Regular maintenance of plant facilities, as recommended in Section 6.8.2.2 of the EIA report, will be performed to confirm the condition of plant facilities and detect any damage for repair or replacement. Training should be provided to the employees on handling accidental spillage, so that in such cases, actions can be carried out quickly to avoid runoff to nearby streams/drains.</p>	Within construction site / During operation phase / Throughout operation phase	OWTF Operator			✓		TM-DSS; Water Pollution Control Ordinance
Waste Management Implications (Construction)									
7.6.1.1	6.3	<p>Good Site Practices</p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> Obtain the relevant waste disposal permits from appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354) and subsidiary Regulations and the Land (Miscellaneous Provisions) Ordinance (Cap. 28); 	Project construction site / Throughout construction stage / Until completion of all construction activities	Contractor			✓		Waste Disposal Ordinance; Regulation and the Land (Miscellaneous Provisions) Ordinance;

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<ul style="list-style-type: none"> ▪ Provide staff training for proper waste management and chemical handling procedures; ▪ Provide sufficient waste disposal points and regular waste collection; ▪ Provide appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; ▪ Carry out regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; ▪ Separate chemical wastes for special handling and disposal to licensed facilities for treatment; and ▪ Employ licensed waste collectors to collect waste. 							Waste Disposal (Chemical Wastes) (General) Regulation; Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site
7.6.1.2	6.3	<p>Waste Reduction Measures</p> <p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> ▪ Design foundation works to minimise the amount of excavated material to be generated; ▪ Provide training on the importance of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling; ▪ Sort demolition debris and excavated materials from demolition works to recover reusable/recyclable portions ▪ Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal ▪ Encourage collection of recyclable waste such as waste paper and aluminium cans by providing separate labelled bins to enable such waste to be segregated from other general refuse generated by the work force ▪ Plan the use of construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste 	Project construction site / Throughout construction stage / Until completion of all construction activities	Contractor	✓	✓			Waste Disposal Ordinance
7.6.1.3	6.3	<p>Excavated and C&D Materials</p> <p>In order to minimise impacts resulting from collection and transportation of C&D material for off-site disposal, the</p>	Project construction site / Throughout construction stage / Until completion	Contractor	✓	✓			Waste Disposal Ordinance ; DEVB Technical

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		excavated materials should be reused on-site as fill material as backfilling material and for landscaping works far as practicable. Other mitigation requirements are: <ul style="list-style-type: none"> ▪ A Waste Management Plan (WMP), which becomes part of the Environmental Management Plan (EMP), should be prepared in accordance with ETWB TC(W) No.19/2005; ▪ A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites) should be adopted for easy tracking; and ▪ In order to monitor the disposal of excavated and non-inert C&D material at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be adopted (refer to DEVB TC(W) No. 6/2010). 	of all construction activities					Circular (Works) No.6/2010 for Trip Ticket System for Disposal of Construction & Demolition Materials; Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site	
7.6.1.4	6.3	Chemical Waste Should chemical wastes be produced at the construction site, the Contractor would be required to register with EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste (such as explosive, flammable, oxidizing, irritant, toxic, harmful, or corrosive). The Contractor should employ a licensed collector to transport and dispose of the chemical wastes, to either the CWTC in Tsing Yi, or any other licensed facilities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Project construction site / Throughout construction stage / Until completion of all construction activities	Contractor		✓			Code of Practice on the Packaging Labelling and Storage of Chemical Wastes; Waste Disposal (Chemical Waste) (General) Regulation
7.6.1.5	6.3	General Refuse General refuse should be stored in enclosed bins or compaction units separated from excavated and non-inert C&D materials. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from inert C&D materials. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Project construction site / Throughout construction stage / Until completion of all construction activities	Contractor		✓			Waste Disposal Ordinance and Public Health and Municipal Services Ordinance - Public Cleansing and Prevention of Nuisances

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
Waste Management Implications (Operation)									
7.6.2.1	6.3	<p>Good site practices</p> <p>Adoption of the following good operational practices should be recommended to minimise waste management impacts:</p> <ul style="list-style-type: none"> ▪ Obtain the necessary waste disposal permits from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Chemical Waste) (General) Regulation and the Land (Miscellaneous Provision) Ordinance (Cap. 28); ▪ Nomination of an approved person to be responsible for good site practice, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site; ▪ Use of a waste haulier licensed to collect specific category of waste; ▪ A trip-ticket system should be included as one of the contractual requirements and implemented by the Environmental Team to monitor the disposal of solid wastes at public filling facilities and landfills, and to control fly tipping. Reference should be made to DEVB TC(W) No. 6/2010. ▪ Training of site personnel in proper waste management and chemical waste handling procedures; ▪ Separation of chemical wastes for special handling and appropriate treatment at a licensed facility; ▪ Routine cleaning and maintenance programme for drainage systems, sumps and oil interceptors; ▪ Provision of sufficient waste disposal points and regular collection for disposal; ▪ Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste, such as covering trucks or transporting wastes in enclosed containers; and, ▪ Implementation of a recording system for the amount of 	Construction site / On a regular basis / Throughout operation stage	OWTF Operator			✓		Regulation Waste Disposal Ordinance; Waste Disposal (Chemical Waste) (General); Regulation and the Land (Miscellaneous Provision) Ordinance; DEVB Technical Circular (Works) No. 6/2010.

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		wastes generated, recycled and disposed of (including the disposal sites).							
7.6.2.2	6.3	<p>Waste reduction measures</p> <p>Adoption of the following good operational practices should be recommended to ensure waste reduction:</p> <ul style="list-style-type: none"> ▪ Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; ▪ Encourage collection of aluminium cans, plastic bottles and packaging material (e.g. carton boxes) and office paper by individual collectors. Separate labelled bins should be provided to help segregate this waste from other general refuse generated by the work force; and ▪ Any unused chemicals or those with remaining functional capacity should be reused as far as practicable. 	Construction site / On a regular basis / Throughout operation stage	OWTF Operator			✓		Waste Disposal Ordinance; Waste Disposal (Chemical Waste) (General); Regulation and the Land (Miscellaneous Provision) Ordinance
7.6.2.3	6.3	<p>Waste generated from pre-treatment process</p> <p>Wastes generated from pre-treatment process should be recycled as far as possible. Wastes generated from pre-treatment process should also be separated from any chemical waste and stored in covered skips. The recyclables should be collected by licensed collectors, while the rest of the waste should be removed from the site on a daily basis to minimise odour, pest and litter impacts. Open burning must be strictly prohibited.</p>	Pre-treatment process / Throughout operation stage	OWTF Operator			✓		Waste Disposal (Chemical Waste) (General)
7.6.2.4	6.3	<p>Chemical Waste</p> <ul style="list-style-type: none"> ▪ Chemical waste generated from machinery maintenance and servicing should be managed in accordance with the Code of Practice on the Packaging, Labelling and storage of Chemical Wastes under the provisions of Waste Disposal (Chemical Waste) (General) Regulation. The chemical waste should be collected by drum-type containers and, when transported off-site, removed by licensed chemical waste contractors. Alternatively, some of the chemical waste may be retained on-site for re-use by the Project in the manufacture of biogas or other products, subject to their composition being confirmed as suitable for such application. 	Construction site Throughout operation stage	OWTF Operator			✓		Code of Practice on the Packaging Labelling and Storage of Chemical Wastes; Waste Disposal (Chemical Waste) (General) Regulation

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<ul style="list-style-type: none"> Plant / equipment maintenance schedules should be planned in order to minimise the generation of chemical waste. Non-recyclable chemical wastes and lubricants should be disposed of at appropriate facilities, such as CWTC. Copies or counterfoils from collection receipts issued by the licensed waste collector should be kept for recording purpose. Recyclable chemical waste will be transported off-site for treatment by a licensed collector. The Contractor will need to register with EPD as a chemical waste producer. 							
7.6.2.5	6.3	<p>General Refuse</p> <ul style="list-style-type: none"> Waste generated in site offices should be reduced through segregation and collection of recyclables. To promote the recycling of wastes such as used paper, aluminium cans and plastic bottles, it is recommended that recycling bins should be clearly labelled and placed at locations with easy access. For the collection of recyclable materials, they should be collected by licensed collectors. General refuse, other than segregated recyclable wastes, should be separated from any chemical waste and stored in covered skips. The general refuse should be removed from the site on a daily basis to minimise odour, pest and litter impacts. Also, open burning of refuse must be strictly prohibited. 	Construction site / On a regular basis / Throughout operation stage	OWTF Operator		✓			Waste Disposal Ordinance
Ecological Impact (Construction)									
8.7	7.3	For precautionary purposes and to further ensure that no wild flora species of conservation interest will be affected, prior to commencement of any construction works, it is recommended to conduct a detailed vegetation survey as baseline monitoring to update the exact locations, number and condition of individuals of <i>Aquilaria sinensis</i> and any other floral species of conservation interest within the Project Area. A Vegetation Survey Report summarizing the findings and recommendations of the detailed vegetation survey should be prepared and submitted to AFCD for approval no later than one month prior to commencement of construction works.	Before Project commencement	OWTF Operator	✓				EIAO-TM
8.7	7.3	During construction phase, erection of a temporary protective	Throughout construction	OWTF Operator		✓			EIAO-TM

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		fence along the plantation area where trees and vegetation, including those of conservation concern identified under the detailed vegetation survey, would be retained within the Project Area is recommended for precautionary purposes to avoid any potential impact from construction activities such as vehicle movement and materials storage. Establishment of the protective fence could also raise the awareness of personnel to be present and protection of the plants. While the protective fence should be properly maintained, monitoring of individuals of <i>Aquilaria sinensis</i> and any other floral species of conservation interest identified in the detailed vegetation survey during construction phase on a monthly basis should be conducted to make sure that they are not affected by the construction works of the Project.	stage						
Ecological Impact (Operation)									
No mitigation measure is required.									
Landscape and Visual Impact (Construction)									
Table 10.7 (CP1)	Table 8.1 (CP1)	Preservation of Existing Vegetation The development proposals would avoid disturbance to the existing trees as far as practicable within the confines of the development site. A preliminary tree survey has been undertaken to establish the existing resources. A tree survey review with formal tree removal application will be submitted to the relevant government departments for approval in accordance with ETWB TC(W) 03/2006 Tree Preservation, during the detailed design phase of the Project. Based on the preliminary findings it would be possible to retain 441 of the existing trees. If possible, all trees which are not in conflict with the proposals would be retained and shall be protected through the means of fencing, where appropriate, to prevent potential damage to tree canopies and root zones from vehicles and materials storage. Specifications for the protection of existing trees will be circulated to the relevant government authorities for approval together with the formal tree removal application.	Construction site / Throughout construction stage / Until completion of all construction activities	Contractor	✓	✓			Technical Circular (Works) No. 3/2006
Table 10.7 (CP2)	Table 8.1 (CP2)	Control of site construction activities <ul style="list-style-type: none"> ■ Storage of materials should be carefully arranged to minimise potential landscape and visual impact. 	Construction site / Throughout construction stage / Until completion	Contractor	✓	✓			EIAO-TM

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<ul style="list-style-type: none"> The location and appearance of site accommodation should be carefully designed to minimise potential landscape and visual impact. Site lighting should be carefully designed to prevent light spillage, Extent of the works area and construction period should be minimised as far as practicable. Screen hoarding with compatible design to blend into the surrounding natural environment should be considered. Temporary works areas should be reinstated at the earliest possible opportunity. 	of all construction activities						
Table 10.7 (CP3)	Table 8.1 (CP3)	<p>Transplantation of existing trees</p> <p>Under current proposal, no tree is recommended to be transplanted since the trees in conflict with the proposed works are not suitable to be transplanted. However, should transplantation be proposed in the detailed design stage after an update tree survey, the recommended final recipient sites should be adjacent to their current locations. Enough time should be reserved for tree transplantation works to increase the survival rate of the transplanting trees. To ensure the survival of transplanted trees, protection work should be considered. The tree transplantation proposal will be submitted to relevant authorities for approval together with the formal tree removal application.</p>	Construction site / Throughout construction stage / Until completion of all construction activities	Contractor	✓	✓			Technical Circular (Works) No. 3/2006
Landscape and Visual Impact (Operation)									
Table 10.8 (OP1)	Table 8.2 (OP1)	<p>Design of the Proposed OWTF</p> <p>OWTF will incorporate design features as part of design mitigation measures including</p> <ul style="list-style-type: none"> Integrated design approach - the location of OWTF should be within the existing Livestock Waste Composting Plant, as far as technically feasible. The location and orientation of the OWTF should be away from landscape and visually sensitive areas such as ponds and woodlands. Building massing – the proposed use of simple responsive design includes having specific height profile requirement 	Construction site / During design stage	Design Consultant / OWTF Operator	✓				EIAO-TM

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		<p>such as, single-storey, lower than the adjacent building structures, and avoiding large built structure for supporting facilities to reduce the intrusion of mass in the rural areas.</p> <ul style="list-style-type: none"> ▪ Treatment of built structures – the structural design should seek to reduce the apparent visual mass of the facilities further through the use of natural materials such as wooden frames or other sustainable materials such as recycled plastics. ▪ Responsive building finishes – Natural tones should be considered for the colour palette for proposed structures. Non-reflective finishes are recommended on the outward facing building facades to reduce glare effect. ▪ Responsive lighting design – Aesthetic design of architectural and lighting with following glare design measures: <ul style="list-style-type: none"> – Directional and full cut off lighting is recommended within the boundaries of OWTF to minimise light spillage to the surroundings; – Minimise geographical spread of lighting, only applying for safety at the key access points and staircases; and <p>Limited lighting intensity to meet the minimum safety and operation requirement.</p>							
Table 10.8 (OP2)	Table 8.2 (OP2)	<p>Amenity / Compensatory Planting</p> <p>Tree retention within the works area is considered to be important. New tree plantings will be concentrated in the proposed amenity areas along the boundaries of the site and along the exterior of OWTF buildings. Although a preliminary planting proposal is not yet available at the moment of producing this EIA Report, anticipated new tree planting within the Project site should be able to fully compensate for the loss of 14 trees proposed to be felled in terms of both quantity and quality. 441 existing trees will be retained through preserving them at their current locations. Establishment of newly planted trees is expected. Trees with high amenity value will be placed along the access routes to provide shade and soften the hard structures of OWTF buildings. Amenity plantings will utilise native tree species found on existing neighbouring slopes or</p>	Construction site / during design and operation stage	Design Consultant / OWTF Operator	✓		✓		Technical Circular (Works) Nos. 7/2002 and 3/2006

EIA Ref.	EM&A Ref.	Environmental Protection Measures	Location / Duration of measures / Timing of completion of measures	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
					Des	Con	Op	Dec	
		woodland areas to improve the ecological connectivity between existing habitats and create a coherent landscape network. Tree species with aggressive roots should be avoided to prevent damage to OWTF buildings and structures. Trees with high or moderate amenity value and low to medium maintenance should be considered as part of landscape resource enhancement. Recommended tree species include <i>Celtis sinensis</i> and <i>Liquidambar formosana</i> . These proposals will be subjected to review at detail design stage of the Project.							
Table 10.8 (OP3)	Table 8.2 (OP3)	Treatment of Slopes In accordance with GEO Publication No. 1/2011 "Technical Guidelines on Landscape Treatment for Slopes", these engineering structures will be aesthetically enhanced through the use of soft landscape works including tree and shrub planting to give man-made slopes a natural appearance, blending into the natural landscape. Whip-sized plantings are preferred on the face of soil cut slopes, at the crest and toe of the slope and within berm planters. These smaller, younger plants can adapt to their new growing conditions quicker than larger sized stock and establish a naturalistic effect rapidly. Recommended tree species include <i>Mallotus paniculatus</i> , <i>Broussonetia papyrifera</i> and <i>Alangium chinense</i> .	Construction site / during design and operation stage	Design Consultant / OWTF Operator	✓		✓		GEO Publication No. 1/2011 "Technical Guidelines on Landscape Treatment for Slopes"
Table 10.8 (OP4)	Table 8.2 (OP4)	Amenity enhancement Rooftop greening and vertical greening to mitigate the visual impact of taller structures can soften the façade of OWTF structures. Frameworks utilised for vertical greening should appear naturalistic.	Construction site / during design and operation stage	Design Consultant / OWTF Operator	✓		✓		Technical Circular (Works) No. 7/2002

Remarks:

1. Des – Design Stage, C – Construction Stage, O – Operation, Dec - Decommissioning
